Waltham Cross Regeneration Work: Progress Updates

	Weekly updates			
		2025		
Date	Location	Description	Photo	
<u>Week</u>	Eleanor Cross	Site clearance.		
ending 4	Monument to		The state of the s	
<u>July</u>	Eleanor Cross	Drainage works.		
	Road	Tree cell works (Excavation, fill and build up). Excavation and preparation for footpath bays at bus station. Kerb and paving installation in front of shopping centre.		
	Eleanor Cross Monument to Park Lane	Planter finishing works. Excavation and preparation for footpath bays. Kerb installation works. Lid setting and paving block installation. Trial hole works		

Excavation preparation for asphalt on footpath on Monarch's Way.

Finishing road trim works to ahead of asphalt pouring on High Street.

Paving installation works.

Drainage works.

Asphalt laid to footpath on Monarchs Way.

Traffic signal box and duct installation.

Kerb installation works.

Tree cell works.

Trial hole works.



Stanhope Road

Planter finishing works.

Drainage works.



Eleanor Cross Monument to Eleanor Cross Road

Site clearance works.

Tree cell excavations works and installation.


Work on street lighting and ducting installation.

Drainage works.

Paving and kerb installation





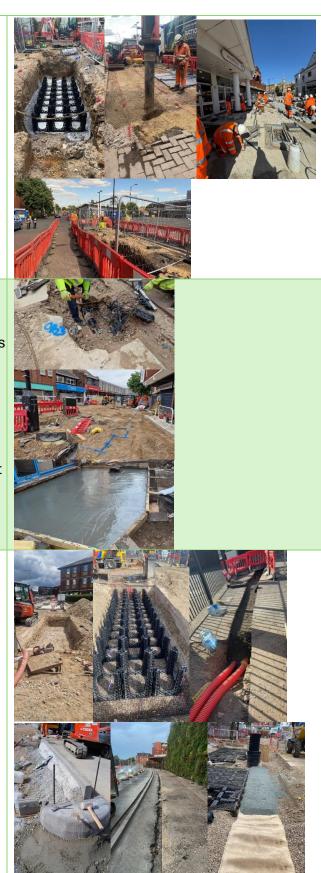

Site clearance and excavation to formation

Planter excavation works and material fill.

Excavation and preparation for footpath bays at shop fronts.

BT Chamber adjustment and repair works.

Park Lane to northern end of the High Street (adjacent to Wickes)

Tree cell excavation and fill works (Material fill and build up).

Excavation and prep for road formation and kerbs.

Kerb and paving installation works.

Excavation and preparation for footpath bays at shop fronts.

Footpath clearance at Monarchs Way.

Kerb installation on Monarchs Way.

	Stanhope Road	Installing traffic signal ducting and sleeves. Excavation ahead of footpath formation at Monarchs Way. Planter excavation works (Material fill and build up).	
Week ending 20 June	Eleanor Cross Monument to Eleanor Cross Road	Site clearance works. Kerb line preparation and installation. Excavation for tree cells. Excavation and preparation for concrete bays and concrete pouring at bus shelter. Paving installed at footpath at bus shelter.	
	Eleanor Cross Monument to Park Lane	Excavation and preparation for footpath bays at shop fronts on east wing. Planter works. Excavating for planters and rain gardens.	More to cut

Park Lane to	Tree cell works.	
northern end	iree cell works.	
	Excavation and	
Street	preparation for road	
(aujacent to	formation.	
VVIUNESI	Setting lids on chambers around site.	
	Kerb and paving	
	installation works.	
	Excavation and	
	preparation for footpath	
	bays at shop fronts.	
	Site clearance to	
	footpath at Monarchs	
	Way.	
	Kerb installation on	
	Monarchs Way.	
	Breaking out kerbs and	
	existing asphalt at	
	footpath on Monarchs	
	Way.	
	Installation of traffic	
	signal ducting and	
	sleeves.	
	Drainage works.	
Road	Planter finishing works.	
	Start of new planter	
	excavation and	
	preparation work.	

Week ending 13 June

Eleanor Cross Monument to Eleanor Cross Road

Continued site clearance at bus station.

Installing electric ducting and sleeves.

Kerb and paving installation.

Kerb installation at bus station.

Footpath bay preparation and concrete pouring.


Drainage works.



Concrete pouring for footpath and parking bays.

Excavation for planters.

Tree cell finishing works.

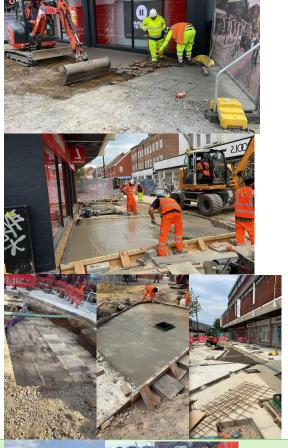

Park Lane to northern end of the High Street (adjacent to Wickes)

Excavation prep for footpath bays at Monarchs Way.

Concrete pouring in footpath bays.

Excavation for kerbs and road to be asphalted.

Street lighting duct installation.


Continued kerb and paving installation near underpass/Wickes.

Planter works.

Road planning works for new kerb line on Monarchs Way.






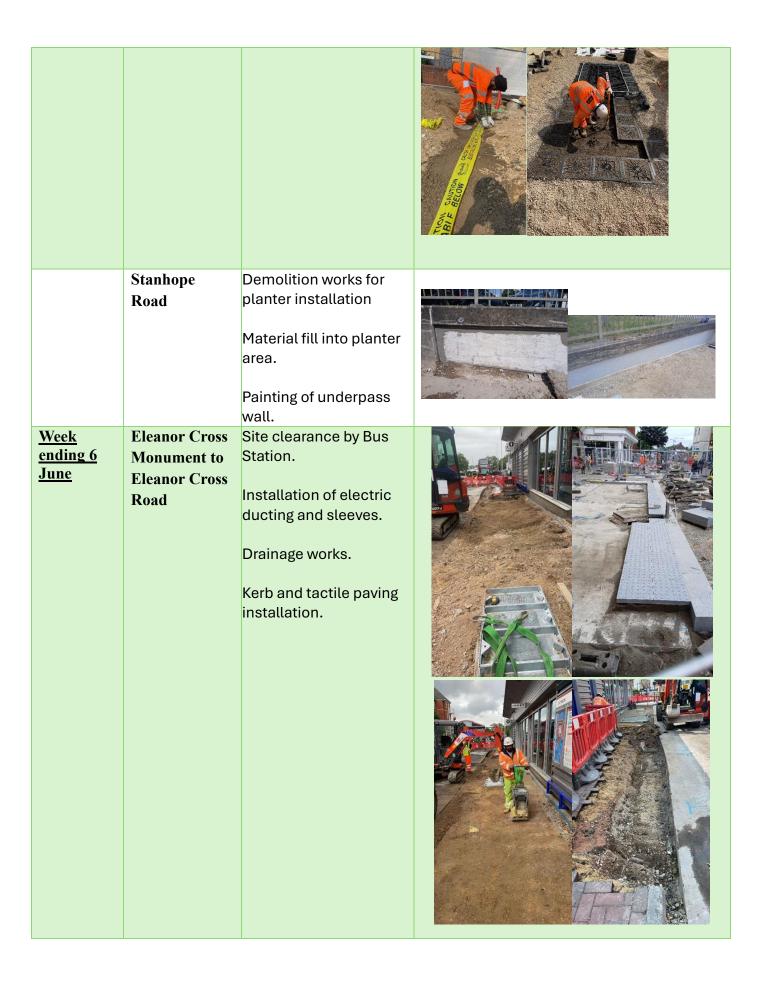

Excavation and preparation for installation of footpath and parking bays.

Concrete pouring on footpath and parking bays.

Finishing works for chamber lids.

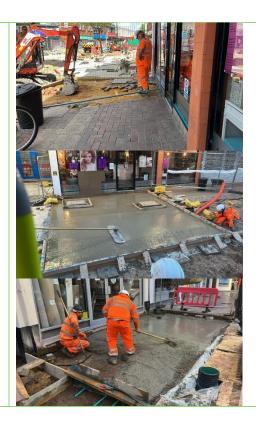

Excavation for footpath bays.

Pouring concrete in footpath bays.

Demolition of underpass walls completed.

Monarchs Way footpath site clearance.

Street lighting ducting installation.

Installation of paving near mobility shop.

Planter works.

Preparation to excavate road for asphalt installation.



Stanhope Road

Finishing works for chamber lids.

Excavation for planters.

Laying binder to footpath.

Kerb installations.



Eleanor Cross Monument to Eleanor Cross Road

Started site clearance at bus station.

Continued excavation and preparation for footpath bays.

Concrete pouring in footpath bays.

Virgin Media chamber adjustment works.

Drainage works.

Street lighting cable installation.



Excavation digs and preparation for footpath bays at Fishpools and shopping centre.

Concrete pouring in footpath and parking bays.

Completion of tree cell works.

Paving and kerb works continued between Fishpools and costa.



Park Lane to northern end of the High Street (adjacent to Wickes)

Tree cell works.

Excavation preparation for footpath bays.

Concrete pouring in footpath bays.

Trial holes for subway wall demolition works.

Subway wall demolition works.

Monarchs Way footpath site clearance.

Cable installation for street lighting installation.



	Stanhope Road	Continuation of paving works.	
Week ending 23 May	Eleanor Cross Monument to Eleanor Cross Road	Installation of streetlight cables. Grading and preparation for binder course. Continued work on footways. Break out and excavation drainage works for gullies installation and connection to mains in the road. UKPN preparation works.	
	Eleanor Cross Monument to Park Lane	Laying paving in road section between Fishpools and Costa Coffee. Concrete pouring on footway bays. Installation of subsoil to tree cells.	CADCET

-

	Park Lane to northern end of the High Street (adjacent to Wickes)	Concrete pouring on road and footway bays. Temporary surfacing in front of the Mobility Shop.	Making Ma
	Stanhope Road	Preparation for footpath bay installation Concrete pouring on footpath bay. Start of kerb edging installation and paving works on the southside.	
Week ending 16 May	Eleanor Cross Monument to Eleanor Cross Road	Excavation and preparation for footpath bays around the shopping centre. Pouring concrete in footpath bays. Break out and excavation of ground for drainage and gullies installation, and connection to the main run in the road. UKPN (UK Power Network) preparation works.	

Paving work between Fishpools and Costa Coffee.

Excavation and preparation for footpath bays in front of Bon Marche, CEX and shopping centre doors.

Concrete pouring in footpath bays in front of Bon Marche, CEX and shopping centre doors.

Site clearance by Fishpools.



Park Lane to northern end of the High Street (adjacent to Wickes)

Drainage works (gullies installation and connections).

Excavation and preparation for road and footpath bays.

Pouring concrete at road and footpath bays in front of La Valle.

Continued underpass demolition works.



Stanhope Road

Preparation for footpath bay installation.

Concrete pouring at footpath bay.

Kerb and edging installation and paving works.





Week ending 9 May

Eleanor Cross Monument to Eleanor Cross Road

Preparation for footpath bays at pharmacy and shopping centre.

Removal of bollards at fire brigade gate for footpath bay preparation.

Excavation for streetlight cables along footpath on southside.

Preparation of footpath for asphalt binder laying.

Drainage excavations for gullies to be installed on the road.



Installation of edgings, laying of paving and grouting in east wing market area and in front of Costa Coffee.

Excavation and preparation for footpath bays in front of Bon Marche.

Pouring of concrete in footpath bays in front of Bon Marche.



Drainage works (installation of gullies).

Excavation and preparation for footpath bays in front of La Valle, in addition to concrete pouring on the footpath.

Continued underpass demolition works.

Stanhope road

Excavation for traffic signal boxes, ducting, signpost sleeves and kerb installation near NHS entrance.

Temporary tarmac laid on Northside near substation to open access for pedestrians.



Week	
ending	2
May	

Stanhope Road

South of Junction

Pedestrian walkways altered.

Excavation and Subbase laid for Footpath construction.

Footpath concrete paving foundations poured.

North of Junction

Clearance of existing footpath and kerb line.

Excavation and Subbase laid for Footpath construction.

New kerb line installed.

Concrete paving foundations poured.



Excavation for kerb braces, parking bays and footpath concrete foundations.

Concrete pours for footpath bays and kerb braces.

Drainage works.

Demolition works to existing subway wall.

New street light network cables installed.



Continued work on high voltage cable diversion and reinstatement.



Eleanor Cross Monument to Park Lane

Footpath paving concrete foundations poured in front of Savers doorway and shop front.

Block Paving installed to Market area.

New street lighting network cable installed.

Removal of existing Street lights.



Eleanor Cross Monument to Eleanor Cross Road

Concrete paving foundations poured in front of shop fronts and doorways at Pavilions Mobile Tech and Handerson's news agents.

Excavation and concrete paving foundation works progressed in front of Pavilions shopping centre and in front on Timpson.

Removal of existing streetlights.



	Eleanor Cross Road	Traffic management layout change. Footpath temporarily reopened. Existing footpath excavated and subbase laid. Clearance of existing block paving. Utility covers set to correct levels.	
Week	Stanhope	Demolition of Existing	
ending 25 April	Road	underpass walls. Subbase laid for Footpath construction. Removal of existing streetlighting. Installation of new street lighting cables. Installation of traffic signal control sockets and foundations. Removal of existing kerb line.	
	Park Lane to northern end of the High Street (adjacent to Wickes)	Excavation for kerb braces, parking bays and footpath concrete foundations. Concrete pours for footpath bays and kerb braces. Drainage works. Demolition works to existing subway wall. New street light network ducts installed.	

	Continued excavation for high voltage cable diversion. High voltage cable diversion.	
	diversion.	
	Lowering of utility chambers.	
Eleanor Cross Monument to	Work progressed further along shop frontages.	
Park Lane	Continued excavation to Footpath in front of Costa coffee.	
	Concrete foundations poured.	
	Excavation to Footpath in front of Savers Phase 1 and concrete foundations poured.	
	New Street lighting network ducts installed.	
	Removal of existing streetlights.	
Eleanor Cross	Works in front of shop	
Monument to	frontages progressed to	
Eleanor Cross	new sections.	
Road	Continued work on	
	excavation of footpath and	
	parking bays, subbase	Land Line and
	laid, and concrete foundations pouring.	
	Removal of existing Street lights.	

	Eleanor Cross	Existing footpath	
	Road	excavated and subbase laid.	
		Tactile crossing installation.	
		Asphalt base course laid.	
		Streetlight network ducting installed.	
		Removal of old street furniture.	
Week ending 18 April	Stanhope Road	Concrete footpath foundations prepped and poured.	
		Traffic signal ducting installed.	
		Demolition of existing subway parapet wall.	
		Site clearance of existing kerb line.	
		Trial holes along existing footpath.	
	Park Lane to	Excavation for kerb	
	northern end	braces, parking bays and	
	of the High	footpath concrete	
	Street	foundations.	
	(adjacent to	Comprete various fair	
	Wickes)	Concrete pours for footpath bays and kerb	
		braces.	
		Drainage works.	
		Demolition works to	
		existing subway wall	Stoney and the state of the sta
		New street light network	
		ducts installed.	
		Trial Holes in	
		preparation of high	
		voltage cable diversion	

voltage cable diversion.

Monument to Park Lane	Work area progressed to shop frontages. Excavation of footpath in front of Costa Coffee. Concrete foundations poured. New street lighting network ducts installed.	COSTA
Monument to Eleanor Cross Road	Works progressed to shop frontages. Excavation of footpath and parking bays to formation and subbase laid.	
Road	New 80 metre Kerb line installed. New street light network ducting installed. New road drainage gullies installed and connected to live main. Footpath widening excavated and subbase laid. Existing footpath excavated and subbase laid.	

Week ending 11 April	Stanhope Rd	Concrete pouring footpath foundations. Cable installation for new traffic lights. Site clearance of infilled underpass.	
	Park Lane to northern end of the High Street (adjacent to Wickes)	Excavation for parking bays, kerb braces and footpath concrete foundations (concrete pouring was also carried out for the last two activities). Continued drainage works and excavation for tree planting areas.	MAZINE MA

	Eleanor Cross Monument to Park Lane	Investigative work in front of Fishpools with trial holes. Trials holes were also drilled to check for drainage. New paved area in front of Fishpools was reopened.	
	Eleanor Cross Monument to Eleanor Cross Road	Pouring of concrete slab for new parking and road bays. Continued excavation and development of the new road, and alignment work for the new kerb.	The Pavilon, High St, Waltham Cross ENG 9PD, UK
	Eleanor Cross Road	Work in this section is being approached in two phases. For the first phase, several activities were undertaken this week including relocation of temporary traffic lights, start of drainage works, clearance of existing kerb lines and installation of new kerb lines.	
Week ending 4 April	Stanhope Road	Excavation of existing footpath and installation of new concrete footpath foundation.	

Excavation for kerb braces, parking bays and footpath concrete foundations.

Concrete pouring for footpath bays and kerb braces.

Street lighting removal and installation of temporary solar powered street lighting.

Continuation of drainage works.



Eleanor Cross Monument to Park Lane

Removal of street lighting and installation of temporary solar powers lighting.

Trial hole drilling to check for existing drainage.

Application of protective sealant to paving.



Eleanor Cross Monument to Eleanor Cross Road

Concrete slab pouring for parking and road bays, and continued excavation and development of the new road.



Eleanor Cross Road

Installation of traffic management. Removal of street lighting, furniture and splitter island.

Following removal of the splitter island, Asphalt was reinstated.





Week ending 28 March

Eleanor Cross Monument to Eleanor Cross Road Road formation work, installation of streetlight cables and sleeves and concrete slab pouring on footpath bays.





Finalised grouting and completed paving and kerbing in front of Fishpools.


Excavation and installation of tree cells in front of the shopping centre.



Excavation for tree cell installation, backfilling of diverted electricity cable, excavation for kerb braces, parking bays and footpath concrete foundations.

Concrete was poured on installed footpath bays and braces.

Drainage works continued and a temporary footpath was set up outside One Beyond.

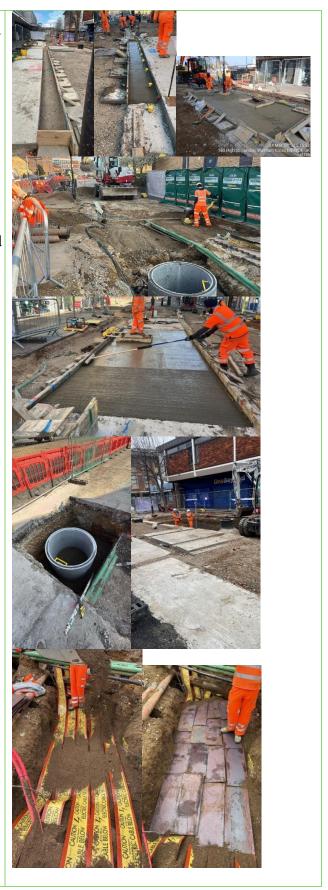

Stanhope Road

Excavation and installation of new traffic light cables and kerbs



Week ending 21 March

Eleanor Cross Monument to Eleanor Cross Road

Removal of existing paving, and excavation for new road and kerb.

Excavation work for new parking bays.



Eleanor Cross Monument to Park Lane

Paving installation in front of Fishpools.

Existing electricity utility diversion work.

Excavation for new tree pits and rain garden drainage.





Continued drainage works and excavation for kerb braces, new road alignment, parking bays and footpath concrete foundations.

Excavation for new tree pits and rain garden drainage.

Diversion of existing electricity utility.
Installation of new street lighting power cables.





	Stanhope Road	Nightime work for drainage installation and new traffic signal cabling installation.	
Week ending 14 March	Park Lane to northern end of the High Street (adjacent to Wickes)	Continuation of drainage works, excavation for kerbs, parking bays and rain gardens. Installation of concrete protection around utilities.	
		Concrete pouring for footpath foundation, and continued work on placement and compaction of road stone. Continued excavation for rain garden.	

Stanhope Road

New paving cleaned and protective sealant installed.

Work fencing was removed and the new pedestrian paving on the northern side of the junction was opened.

Preparation on the opposite side of the road for drainage and kerb works next week.



Eleanor Cross Monument to Park Lane

Concrete pour on footpath bays, drainage works and installation of new cables.

Preparation works in front of Fishpools to begin work on kerbs, edgings and block paving next week.

		Continued excavation for electricity cable diversion and excavation for new planter area.	
	Eleanor Cross Monument to Eleanor Cross Road	Drainage works (saddle connections to carrier drainage pipe). Site clearance in preparation for more drainage work next week.	
Week ending 7 March	Stanhope Road	Continued installation of new paving.	



	Existing utility cables lowered to enable road construction. Laying of road stone.	
Monument to	Additional pedestrian crossover points temporarily installed	
	Excavation to divert high voltage electricity cable	
	Cable ducting work to new street lighting installation.	

		Continued work on concrete pouring on road and footpath bays, and excavation for planter area has started.	
	Eleanor Cross Monument to Eleanor Cross Road	Continuation of drainage works and trial excavations to locate existing utility pipes	
Week ending 28 February	Northern end of the High Street (new pedestrian crossings)	Continuation of paving slab installation at the new crossing point in Stanhope Road	
	Northern end of the High Street (underpass)	Work has continued to backfill de now decommissioned underpass at Monarchs Way	

	Park Lane to northern end of the High Street (adjacent to Wickes)	Continuation of work to lower existing utility ducts to accommodate new road surface.	
	Eleanor Cross Monument to Park Lane	Concrete started to be poured along the High Street to serve as the new road foundation. Preparation work has continued to install new paving outside Fishpools.	SALE SALE SALE SALE SALE SALE SALE SALE
Week Ending 21 February	Stanhope Road	Continued work on new paving installation, including the addition of tactile paving.	

Park Lane to northern end of the High Street (adjacent to Wickes) Work on breaking down the ramps that used to serve the former underpass has continue alongside backfilling to bring the ramp up to street level.



Park Lane to northern end of the High Street (adjacent to Wickes) Lowering of existing utility ducts to accommodate new road surface.



Old paving removed from outside Fishpools.
Concrete bays have been installed outside the shop, these will support the new foundation and paving.







Week Ending 14 February	Stanhope Road	New paving slabs installed at the new pedestrian crossing.	
	northern end of the High Street (adjacent to Wickes)	Infilling of former underpass ramp section with stones. This is being done to bring this section up street level.	
	Park Lane to northern end of the High Street (adjacent to Wickes)	Continued excavation work for new drainage runs. This is progressing well with 90% of the drainage now installed.	

	Eleanor Cross Monument to Park Lane	Concrete base for the new road was poured and levelled. These new concrete bays will serve as the foundation for the new paving slabs.	
Week Ending 7 February	Stanhope Road	Concrete foundations for the new pedestrian crossing laid. Traffic light bases installed and tested.	
	Park Lane to northern end of the High Street (adjacent to Wickes)	Continued excavation for installation of drainage runs along this location.	
	Eleanor Cross Monument to Park Lane	Installation of shutter frames on the ground to support the paving's concrete foundations.	DRING COLAMANCE COLA

Week	Stanhope	Started to install concrete	
Ending 31 January	Road	foundations to connect the new paving (also being installed) to the new pedestrian crossing.	
	Stanhope Road	Continued work to break up ramp that serviced the underpass. At the same time, drainage is also being installed next to the former underpass.	
	Park Lane to northern end of the High Street (adjacent to Wickes)	Continued excavation and installation of new drainage.	
	Eleanor Cross Monument to Park Lane	Continued work on the installation of concrete foundations for the new road. Ground levelling work in ongoing along with installation of bases for new lighting columns.	

Week Ending 24 January	Stanhope Road	Decommissioned underpass has been filled with concrete. Work in progress to break up the concrete ramps that serviced the underpass ahead of filling these sections.	
	Stanhope Road	Kerbs have been installed in preparation for concrete pouring for new street foundations.	
	Stanhope Road	Ground preparation work to install the new pedestrian crossings has commenced.	
	Park Lane to northern end of the High Street (adjacent to Wickes)	Drainage installation	
	Eleanor Cross monument to Park Lane	Drainage work in this section has been completed. Concrete started being poured for foundation of the new road	

Week Ending 17 January	Stanhope Road	Work on filling underpass has commenced. This work took three days to complete.	
			14 Jan 2025 10:37:32 1282 Stanhope Road Hustordshire
Week ending 10 January	Stanhope Road	Wooden shutters installed in underpass to support concrete filling.	13 Dec 2024 11:21:41 39a King Edward Road Hertfordshire England
	Park Lane to northern end of the High Street (adjacent to Wickes)	Start of planned drainage installation to go around existing utilities.	
	Eleanor Cross Road Monument to Park Lane	Excavation for new road foundation and streetlights as well as ducting to power new streetlights.	

2024				
		Week ending 13 D	ecember	Monar
	Road	Pipes and ducting installed at Monarchs Way underpass. Work commenced to install shutters that will retain the concrete which is to be poured in a few weeks.		
	Park Lane to Monarchs Way	Investigative work for existing utility duct that needs to be lowered in this area.		

	Eleanor Cross Road Monument to northern end of the High Street (adjacent to Wickes)	Digging to accommodate foundations of the new road commenced. Work to lower existing	
	Road Monument to Park Lane	utility duct ahead of new pavement installation. Continuation of drainage installation.	Before
Week ending 6 December	Monarchs Way	Road works on Monarchs Way completed.	
	Stanhope Road	Preparation ahead of disconnection of electrical services in the underpass linking Stanhope Road with the High Street.	ADVANCE WARNING Monarchs Way underpass will permanently close on Mon 9 December splease use the pedestriane confliction of the underpass) Were Info: WWW.Norzbourne.gov.uk

	Park Lane to Monarchs Way	Removal of existing paving and setting out of new lines for proposed drainage locations.	
	Eleanor Cross Monument to Park Lane	Continued work to lower existing utility ducts, and work to start reducing the existing ground to the correct level for the new road.	
Week ending 29 November	Stanhope Road	Installation of new kerbs and bases for the new traffic lights.	
	Park Lane to Monarchs Way	Extension of fencing lines ahead of removal of existing pavement.	
	Monarchs Way	Drainage installation completed.	

	Northen end of the High Street	Section of drainage installation completed.	
	Near Queen Eleanor Monument Towards northern end of the High Street	Lowering of existing utility duct, and continued installation of drainage.	
	From Eleanor Cross Monument to Park Lane	Completion of gas main installation and backfilling, and removal of fencing from related section.	
Week ending 22 November	Stanhope Road	Excavations on the South Bound Carriageway to install the new kerb line and, excavations to allow the new traffic lights to be powered. In tandem, excavations have also commenced on the opposite side, (next to Wicks) for drainage and new kerbs.	

	Fishpools/High	Preparation ahead of final	
	Street to	connection of gas main,	
	Eleanor Cross	with testing and	
	Road	backfilling continuing in	
	Noau	tan Jama	
		tandem.	
	N Y (1) 1	5	
	Northern end	Drainage installation	
	of the High	planning to avoid existing	
	Street	utilities	
	From Eleanor	Continuation of drainage	A THE STATE OF THE
	Cross		
		installation	
	Monument to		
	Park Lane		
			(a) The state of the second
**7	C/ I	XX7 11	
Week	Stanhope	Works on the new	
ending 15	Road	pedestrian crossing	Woles
November			

	From Fishpools/High Street to Eleanor Cross Road	Backfilling and testing of installed gas main	
	Northern end of High Street from Waltham Cross Bakery to Wicks	Vacuum excavation ahead of drainage installation.	
	From Eleanor Cross Monument to Park Lane	Excavation to reveal existing ducts and pipes, ahead of installation of new ones.	14 Nov 2024 16:16:51 133 High Street Hertfordshire England
Week ending 8 November	Monarchs Way	New Manhole was installed within the north bound carriage way	
	Stanhope Road	Installation of manholes. In addition, installation of ducts and pipes to feed new traffic light electricity continues.	
	Eleanor Cross Road.	Continued work on new gas main installation	
	From Fishpools/High Street to Park Lane.	Installation of drainage manholes and subsequent extension of fencing along the High Street.	

Week	Monarchs	Excavation work to	
ending 1	Way	expose existing drainage	
November	''ay	network, ahead of	
Tiovenibei		connection with new	
		drainage and manhole.	
	Stanhope	Continued installation of	
	Road	drainage, ducting and	
	Kuau	paving.	
	From	Continuation of gas main	
	Fishpools/High	diversionary works.	
	Street towards	dry crarenary werns.	
	Eleanor Cross		
	monument.		
	From Eleanor	Completion of drainage	
	Cross	installation. Drainage	
	monument	installation work towards	
	towards	Park Lane is ongoing.	
	Fishpools	and Lane is ongoing.	
	1, 1211hani2		
Week	Stanhope	Kerb removal and start of	ContractConsison
ending 25	Road	drainage installation,	Stanhope Road – works to new crossing – Footpath
October	Roau	ahead of installation of	closure
October		new pedestrian crossing.	3 Wickes Walk-om Cross Home improvement abop Primary School 9 9 9 9 9 9 9 9 9 9 9 9 9
		new pedestrian crossing.	Drainage excavations
			Waltham Cross Street Excavations to expose
			and remove existing Gas Main
			Gas Main Park En Pa
			Park En Shopping Chitre Shopping Chitre
			Hammonds Fitted Bedroom Furniture
			Hammonds W Fitted Wardrobes Halifay Fitted Wardrobes
			KFC Waltham Cross Eleanor Cross Road
			VS A
			TFC Waltham Cross
	From Eleanor	Excavation work for	Contract Consider
		existing gas main	Stanhope Road – works to new crossing – Footpath
	Cross	diversion.	Olosure Wickes William Cross Four Swannes Four Swannes Four Swannes Four Swannes Four Swannes Four Swannes
	Monument to	GI (OI DIOII.	
	Eleanor Cross		Drainage excavations
	Road		Waltham Cross Street Excavations to expose
	n n	D ' ' ' 11 .'	Gas Main Results Sainsbury's Gas Main Results Sainsbury's Gas Main
	From Eleanor	Drainage installation	pavilions Pavilions
	Cross	started.	Shopping Centre Shopping Cytre
	monument to	T (* (* 1	Hammonds Fitted
	Park Lane	Investigative work to	Ave Filter Wald Obes
		prevent damage to	KFC Waltham Cross Road Deleanor Cross Road Del
		existing cables. This	VS TFC Waltham Cross Q
		works will continue in	T T T T T T T T T T T T T T T T T T T
		tandem with drainage	
		installation.	

12 September	High street – near Skills Hub	Groundbreaking event was held to mark the start of the works.	
From 4 September	Northen end of the High Street, including Waltham Cross High Street Car Park.	Site preparation – cordoning off and removal of street furniture.	TO PROJECT
