




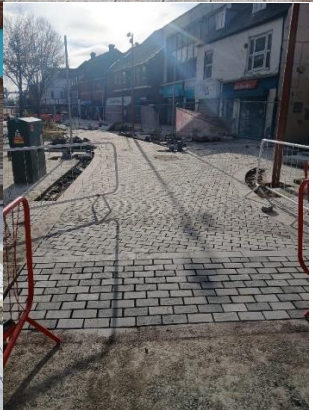








Waltham Cross Regeneration Work: Progress Updates

Weekly updates			
2025			
Date	Location	Description	Photo
<u>Week ending 14 November</u>	Park Lane	Kerbing work.	
		<p>Block paving installation on footpath.</p> <p>Tactile paving installation.</p> <p>Road trimming</p> <p>Swing gate post installed.</p>	
	Eleanor Cross Monument to Park Lane	<p>Installation of Cycle stands.</p> <p>Rain garden temporary fencing installation.</p> <p>Block paving installation.</p> <p>Light column installation.</p> <p>Sealing shop fronts and installation of lids.</p>	

			   
	Eleanor Cross Monument to Eleanor Cross Road	<p>Rain garden temporary fencing installation, resin preparation and planting.</p> <p>Swing gate post installation.</p> <p>Block paving installation to footpaths.</p> <p>Setting lids to chambers.</p> <p>Pedestrian guardrail installation.</p> <p>Sealing shop fronts and lids.</p> <p>Tactile paving installation.</p>	   

<p><u>Week ending 14 November</u></p>	<p>Park Lane</p>	<p>Kerbing works.</p>	
	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Rain garden planting and infill.</p> <p>Block paving installation on footpaths.</p> <p>Street furniture installation.</p> <p>Rain garden resin preparation.</p> <p>Setting lids o chambers.</p> <p>Sealing shopfronts.</p> <p>Opening access for pedestrians.</p> <p>Edgings in road.</p>	
	<p>Eleanor Cross Monument to Park Lane</p>	<p>Defect reinstatements.</p> <p>Rain garden infill and planting.</p> <p>Rain garden resin preparation.</p> <p>Edgings tie in.</p> <p>Block paving installation on footpaths.</p>	

		<p>Setting lids to chambers.</p> <p>Street furniture installation.</p> <p>Opening access for pedestrians.</p> <p>Street lighting works.</p> <p>Sealing shopfronts.</p> <p>Paving wash.</p>	 
	<p>Eleanor Cross Monument to Eleanor Cross Road</p>	<p>Rain garden infill and planting.</p> <p>Block paving installation.</p> <p>Road and footpath works.</p> <p>Street lighting works.</p> <p>Defect reinstatement.</p> <p>Opening access for public.</p> <p>Tactile paving installation.</p> <p>Preparation of rain garden resin.</p> <p>Sealing shop fronts.</p> <p>Pedestrian guardrail installation.</p>	  

**Week
ending 7
November**

Park Lane

Kerbing work.



**Park Lane to
northern end of
the High Street
(adjacent to
Wickes)**

Block paving
installation.

Setting lids to
chambers.





Surfacing road.

Opening access for
pedestrian.



Street furniture
installation.




Concrete bay
pouring.





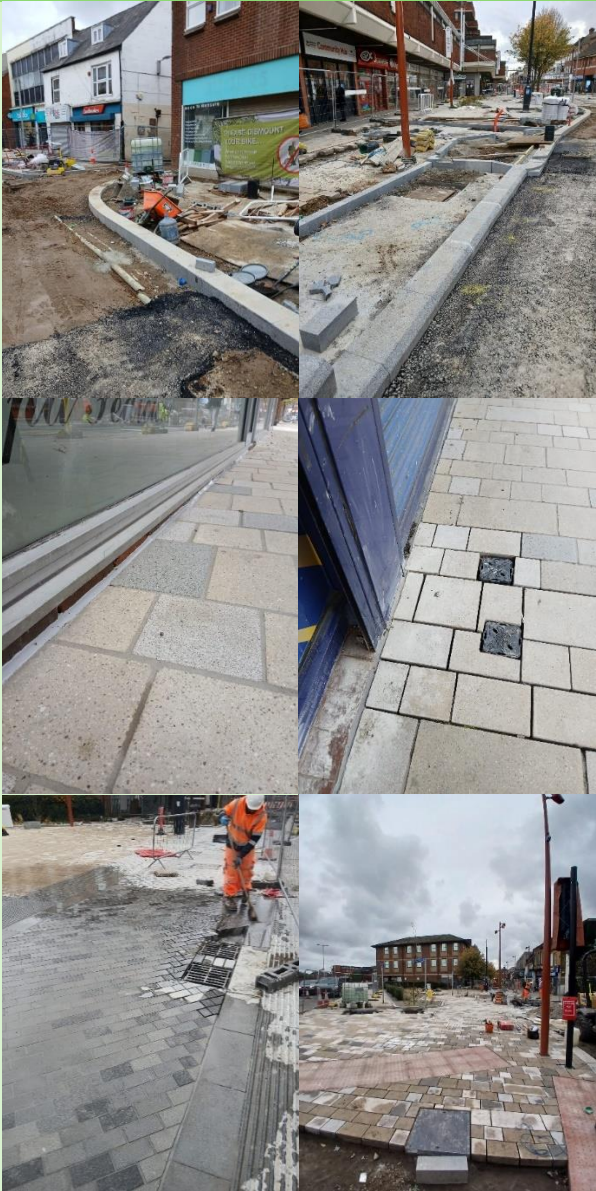


			
	Eleanor Cross Monument to Park Lane	<p>Yorkstone and block paving installation on footpaths.</p> <p>Rain garden resin preparation and pouring.</p> <p>Setting lids to chambers.</p> <p>Fencing adjustment for pedestrian access.</p> <p>Pouring of concrete bays.</p> <p>Street furniture installation.</p> <p>Resin preparation and pour for rain gardens.</p>	  


	<p>Eleanor Cross Monument to Eleanor Cross Road</p>	<p>Tactile paving installation.</p> <p>Block paving installation on road.</p> <p>Footpath surfacing.</p> <p>Light column works.</p> <p>Installation of block paving on footpaths.</p> <p>Rain garden infill.</p> <p>Setting lids to chambers.</p> <p>Installation of pedestrian guardrail.</p> <p>Resin preparation and pour for rain gardens.</p> <p>Installation of Street furniture.</p> <p>Feeder pillar works.</p>	
<p><u>Week ending 31 October</u></p>	<p>Monarchs Way</p>	<p>Painting cycle path.</p> <p>Surfacing cycle path.</p>	




	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Block paving, special kerbs and edgings installations.</p> <p>Block paving tie in.</p> <p>Sealing shopfronts.</p> <p>Footpath tie in.</p> <p>Raingarden infill and planting.</p> <p>Surfacing works.</p> <p>Concrete slab preparation and pouring.</p> <p>Street furniture installation.</p>	
	<p>Eleanor Cross Monument to Park Lane</p>	<p>Concrete slab preparation and pouring.</p> <p>Kerb and paving installation.</p> <p>Block paving tie ins.</p> <p>Sealing shopfronts.</p> <p>Raingarden infill and special edging work.</p>	



		<p>Shuttering work for epoxy on raingardens.</p> <p>Street furniture installation.</p> <p>Setting lids to chambers</p>	
	<p>Eleanor Cross Monument to Eleanor Cross Road</p>	<p>Block paving, edging and kerb installations.</p> <p>Road surfacing works.</p> <p>Road lining installation.</p> <p>Footpath surfacing works.</p> <p>Installation of pedestrian guardrail.</p> <p>Street furniture installation.</p> <p>Feeder pillar works.</p>	
<p><u>Week ending 24 October</u></p>	<p>Monarchs Way and Stanhope Road</p>	<p>White lining and cycle lane completion works.</p> <p>TM alteration for completion.</p> <p>Installation of road studs.</p> <p>Road surfacing works.</p>	

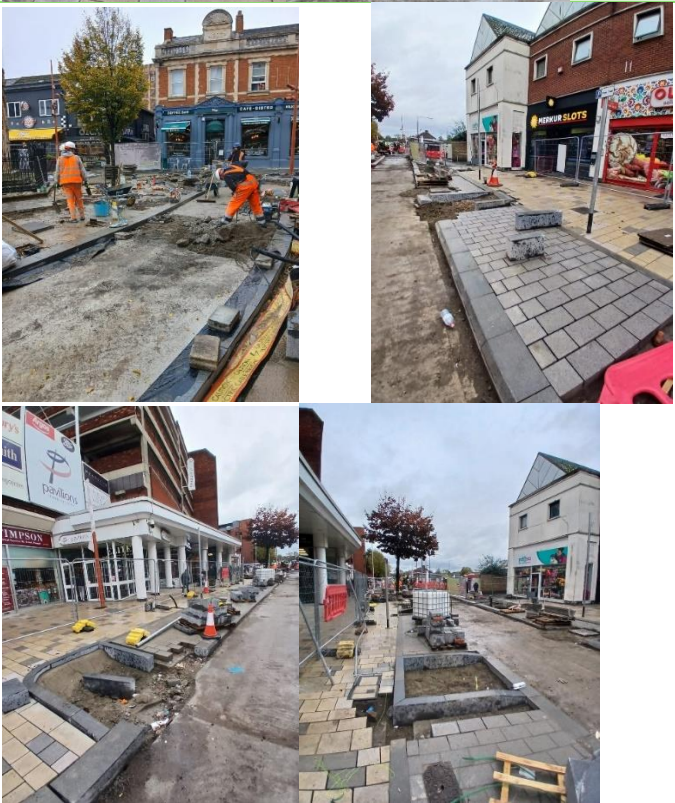

	Park Lane	Kerbing installation.		
	Park Lane to northern end of the High Street (adjacent to Wickes)	<p>Concrete bay preparation and pouring.</p> <p>Manhole backfill to trim.</p> <p>Road trimming.</p> <p>Block paving tie ins.</p> <p>Block paving footpath installation.</p> <p>Setting lids to chambers.</p> <p>Rain garden infill and planting.</p> <p>Cutting carriageway for paving.</p>		
	Eleanor Cross Monument to Park Lane	<p>Paving tie ins.</p> <p>Rain garden infill and planting.</p> <p>Special kerbing installation.</p> <p>Setting lids to chambers.</p>		


			
	Eleanor Cross Monument to Eleanor Cross Road	<p>Paving, footpath and parking bay work.</p> <p>Planed road.</p> <p>Installation of radial kerbs around rain gardens and footpaths.</p> <p>Installation of pedestrian guardrails.</p> <p>Signpost installation.</p> <p>Light column works.</p> <p>Base and binder added to footpaths.</p> <p>Setting lids to chambers.</p> <p>Splitter island installed.</p> <p>Drainage works.</p>	

<p><u>Week ending 17 October</u></p>	<p>Monarchs Way</p>	<p>White lining installation.</p> <p>Road surfacing and substation works.</p> <p>Work on paving and footpath.</p>	
	<p>Park Lane</p>	<p>Road trimming and kerbing installation.</p>	
	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Installation of block paving, raingarden and special edgings.</p> <p>Settings lids to chambers.</p> <p>Road trimming work.</p> <p>Planting inside raingardens.</p>	

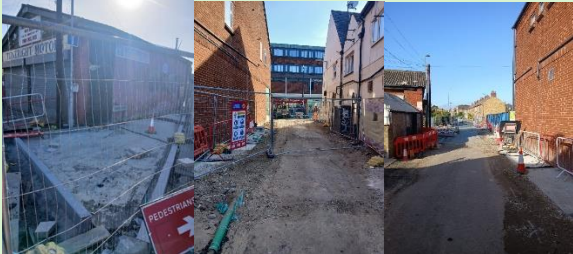		<p>Tactile paving work.</p> <p>Drainage chamber work and infill.</p>		
	<p>Eleanor Cross Monument to Park Lane</p>	<p>Block paving and kerbing installations.</p> <p>Feeder pillar work.</p> <p>Concrete bay preparation.</p>		
	<p>Eleanor Cross Monument to Eleanor Cross Road</p>	<p>Kerbing, raingarden and edging installations.</p> <p>Excavation and fill work.</p> <p>Light column installation.</p> <p>Footpath paving.</p> <p>Bus station radius kerbs and footpath work.</p> <p>Work on pedestrian guard rail at the bus station.</p>		

<p><u>Week ending 10 October</u></p>	<p>Monarchs Way</p>	<p>Work on feeder pillar.</p> <p>Rain garden completions.</p> <p>Traffic signal pole and head installation.</p> <p>Cabling works.</p> <p>Installation of road signage.</p>	
	<p>Park Lane</p>	<p>UKPN cable lowering work.</p> <p>Installation of road trimming, kerbing and tactile paving preparation work.</p>	
	<p>Eleanor Cross Monument to Park Lane</p>	<p>Installation of edgings around rain gardens.</p> <p>Block paving footpath and carriageway installations.</p> <p>Rain garden fill.</p> <p>Feeder pillar works.</p> <p>UKPN cable lowering work.</p> <p>Site clearance for works.</p> <p>Lighting connections.</p>	

		Lids installation on chambers.	
	Eleanor Cross Monument to Eleanor Cross Road	<p>Installation of block paving footpaths.</p> <p>Work on kerbing and edgings.</p> <p>Light column installation.</p> <p>Excavation and Infill of rain gardens.</p> <p>Footpath works.</p> <p>Electrical ducting.</p> <p>Bus station radius breakout and kerbing.</p> <p>Installation of signs.</p> <p>Drainage works.</p>	
<u>Week ending 3 October</u>	Monarchs Way	<p>Work on traffic signal ducting for loops.</p> <p>Traffic lights installed.</p> <p>Rain garden and planter planting.</p>	

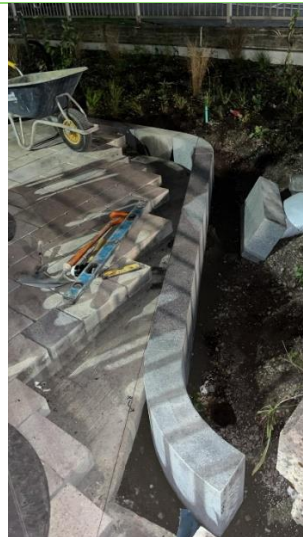

Park Lane

Concrete bay preparation and pour.

Kerbs installed.



Park Lane to northern end of the High Street (adjacent to Wickes)

Block paving installation.

Rain garden kerbing and infill.



UKPN (utility cable) diversion work.



Feeder pillar base and cabinet.



Tactile paving installation.

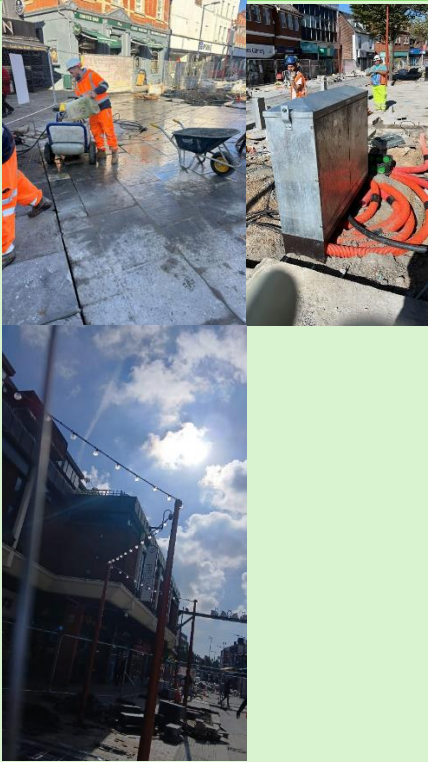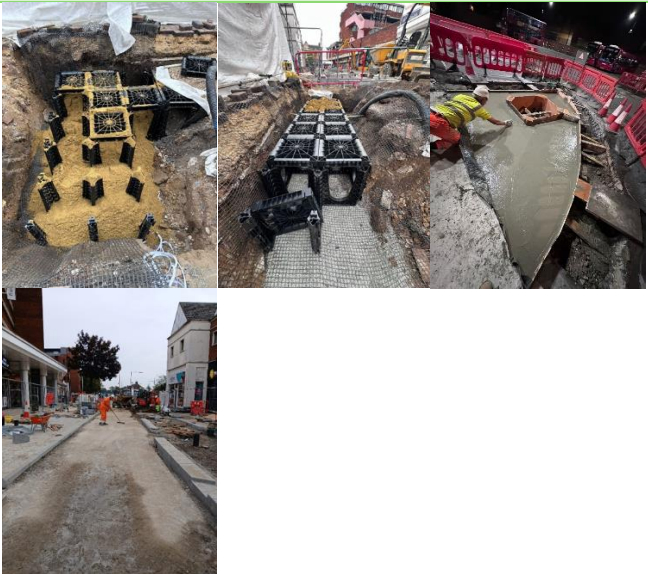Tree surround block paving.





		Lids installed on chambers.	
	Eleanor Cross Monument to Park Lane	<p>Installation of light column lanterns.</p> <p>Feeder pillar cabinet and base.</p> <p>Block paving tie-ins.</p> <p>Installation of lids on chambers.</p> <p>UKPN diversion (utility cable).</p>	
	Eleanor Cross Monument to Eleanor Cross Road	<p>Block paving.</p> <p>Kerbs installed along carriageway and around raingarden and planter areas.</p> <p>Outer roundabout at KFC footpath.</p> <p>Concrete bay pours.</p> <p>Yorkstone restored.</p> <p>Raingarden and treecell install.</p>	

		<p>Bus station radius break-out and bay pour.</p> <p>Splitter island paving Sleeve and ducting.</p>		
<p><u>Week ending 26 September</u></p>	<p>Monarchs Way</p>	<p>Traffic signal ducting installation.</p> <p>Garden and planter vegetation.</p>		
	<p>Park Lane</p>	<p>Preparation and pouring of concrete slab at entrance to Park Lane.</p> <p>Gully connections into chamber.</p>		

	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Base and binder installed along carriageway.</p> <p>Block paving installation along footpaths.</p> <p>Clearance for raingarden and planter area infill.</p> <p>Illuminated signs and light column works.</p> <p>Gully and chamber lids set.</p> <p>In-ground units installed and paved.</p> <p>Tactile paving installed.</p>	
	<p>Eleanor Cross Monument to Park Lane</p>	<p>Light column and lantern installation.</p> <p>Block paving installation.</p> <p>Site clearance.</p> <p>Feeder Pillar installation.</p>	

	<p>Eleanor Cross Monument to Eleanor Cross Road</p>	<p>Rain gardens kerb and edging installation.</p> <p>Rain garden excavation and backfilling.</p> <p>Bus station radius extension.</p> <p>Block paving installation.</p> <p>Light column installation.</p> <p>Splitter island paving completion.</p> <p>Concrete bays poured.</p> <p>Streetlight ducting from monument down Eleanor Cross Road.</p> <p>Preparation for paving works around monument.</p> <p>Parapet extension over subway.</p>	        
<p><u>Week ending 19 September</u></p>	<p>Monarchs Way</p>	<p>Traffic signal ducting.</p> <p>Preparation works for surfacing.</p> <p>Planter works on splitter.</p>	

	<p>Park Lane</p> <p>Gully Connections into existing manhole.</p> <p>Backfilling against concrete slabs.</p> <p>Existing footpath removed.</p> <p>Preparation for kerbs.</p> <p>Footpath bays poured and prepared.</p>	
	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p> <p>Light columns installed.</p> <p>Block paving installation.</p> <p>Kerbing installation around rain gardens and carriageway.</p> <p>Ducting for street lighting.</p> <p>In-ground units set.</p> <p>Traffic signal cable pulled.</p>	
	<p>Eleanor Cross Monument to Park Lane</p> <p>In-ground units installed.</p> <p>Block paving.</p> <p>Kerbing around rain gardens.</p> <p>Kerbs along the carriageway.</p> <p>Ducting connections.</p>	

	<p>Eleanor Cross Monument to Eleanor Cross Road</p>	<p>Block paving works.</p> <p>Kerbs installed across carriageway and around rain gardens.</p> <p>Preparation and installation of lighting columns.</p> <p>Binder installed on footpath opposite bus station.</p> <p>Paving of splitter island at KFC.</p> <p>Rain garden drainage.</p> <p>In-ground unit installation.</p> <p>Ducting and sleeves installed.</p> <p>Concrete bay installation.</p>	
<p><u>Week ending 12 September</u></p>	<p>Monarchs Way</p>	<p>Site clearance.</p> <p>Preparation works for asphalt and tarmac top in central reservation.</p> <p>Asphalt laid to central reservation.</p> <p>Blacktop layer laid on central reservation.</p> <p>Kerb and paving installation works at Splitter.</p>	



Park Lane

Site clearance.

Preparation and pouring of concrete on footpath bays.

UKPN cable lowering works.



Park Lane to northern end of the High Street (adjacent to Wickes)


Installation of footpath concrete bays.





Paving works.


In-ground unit excavation preparation works.

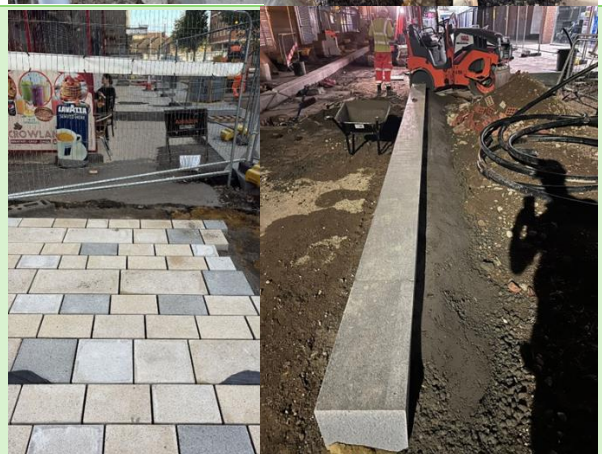


Kerb installation works.

Road preparation works for asphalt.

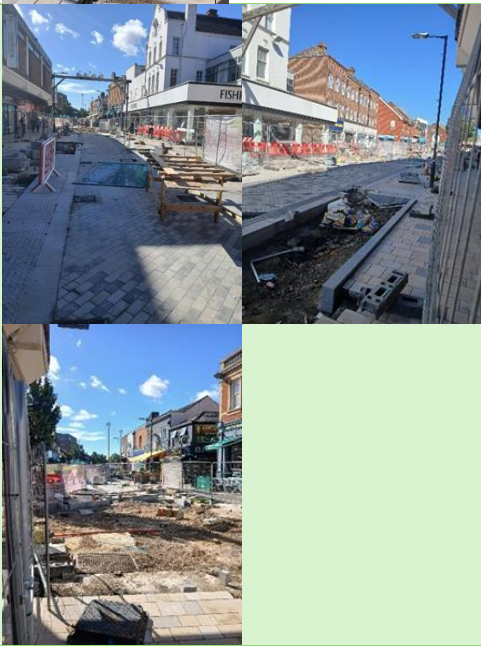

		Chamber and gully buildup and finishing works.	
	Eleanor Cross Monument to Park Lane	<p>Site clearance.</p> <p>Kerb installation works.</p> <p>Concrete pouring on road and installation of concrete footpath bays.</p> <p>Paving works.</p>	  
	Eleanor Cross Monument to Eleanor Cross Road	<p>Site clearance.</p> <p>Rain garden works opposite bus station exit.</p> <p>Excavation and preparation for footpath bays around monument.</p> <p>Kerb installation works at rain garden.</p> <p>In-ground unit excavation works.</p> <p>Installation of binder and tarmac top at splitter island.</p>	  
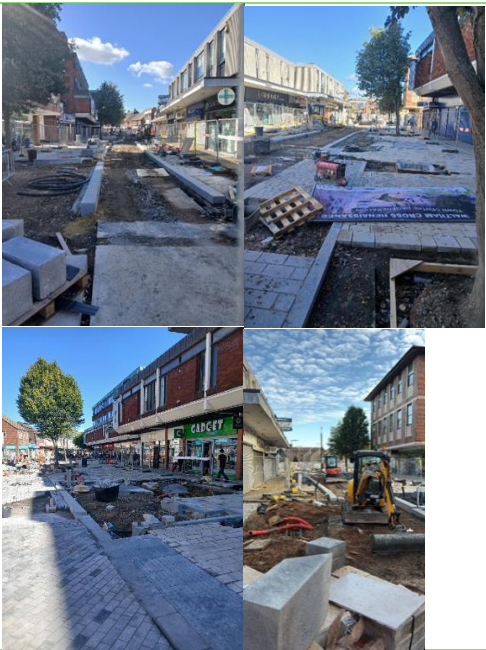
<p><u>Week ending 5 September</u></p>	<p>Eleanor Cross Monument to Eleanor Cross Road</p>	<p>Site clearance.</p> <p>Drainage works.</p> <p>Rain garden preparation works opposite bus station exit.</p> <p>Excavation and preparation for footpath bays around monument.</p> <p>Kerb installation works at Eleanor Cross Road and tie into Monarch's Way.</p>	
	<p>Eleanor Cross Monument to Park Lane</p>	<p>Kerb installation works.</p> <p>Prepped and poured footpath bays.</p> <p>Paving works.</p> <p>Setting lids on utility and drainage chambers.</p>	

	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Prepping and pouring footpath concrete bays.</p> <p>Paving works.</p> <p>Rain garden buildup finishing works.</p> <p>Kerb installation works.</p>	
	<p>Park Lane</p>	<p>Site clearance.</p> <p>Prepping for UKPN diversion/protection works.</p>	
	<p>Monarchs Way</p>	<p>Excavation and preparation for surfacing in centre reservation.</p> <p>Kerb installation at bottom end of centre reservation at KFC roundabout.</p> <p>Kerb installation at Eleanor Cross Road splitter going onto roundabout.</p> <p>Planter excavation works at splitter.</p> <p>Drainage works.</p>	

**Week
ending 29
August**

**Eleanor Cross
Monument to
Eleanor Cross
Road**

Site clearance.



Drainage works.


Rain garden
preparation works
opposite bus
station exit.


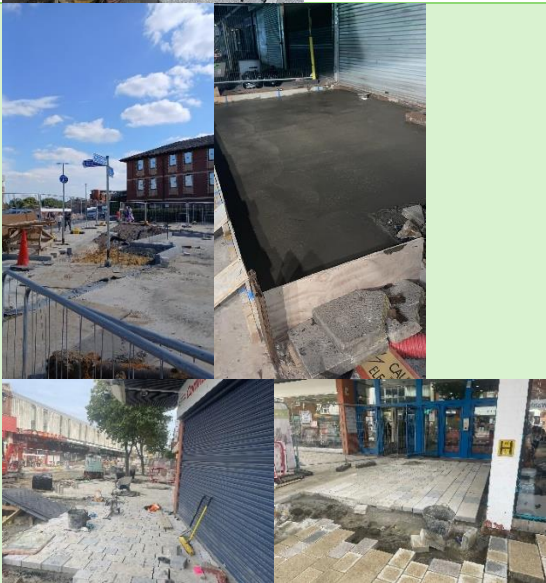
Excavation and
preparation for
footpath bays
around monument.



Kerb installation
works at KFC tie
into Monarchs
Way.



	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Prepping and pouring footpath concrete bays.</p> <p>Paving works.</p> <p>Finishing work for rain gardens.</p> <p>Kerb installation works.</p>	
	<p>Park Lane</p>	<p>Site clearance.</p> <p>Prepping and pouring footpath bays.</p>	
	<p>Eleanor Cross Monument to Eleanor Cross Road</p>	<p>Site clearance.</p> <p>Excavation preparation for surfacing work.</p> <p>White lining work on the carriageway.</p> <p>Kerb installation works.</p> <p>Planter excavation works.</p> <p>Drainage works.</p>	

<p><u>Week ending 22 August</u></p>	<p>Eleanor Cross Monument to Eleanor Cross Road</p>	<p>Continued construction of new splitter island at KFC.</p> <p>Replacement of damaged drainage kerbs.</p> <p>New road gully installation.</p> <p>New drainage network installation at KFC/approach to roundabout.</p> <p>New footpath construction and binder asphalt course.</p> <p>Ducting and foundation works.</p> <p>Excavation of tree bit on new splitter island.</p> <p>Kerb installation on new splitter island.</p> <p>Drainage kerb installation at KFC/approach to roundabout.</p> <p>Footpath concrete foundation at monument area.</p>	
--	--	---	--

	Eleanor Cross Monument to Park Lane	<p>Kerb installation works.</p> <p>Paving works.</p> <p>Installation of utility and drainage chamber covers.</p>	
	Park Lane to northern end of the High Street (adjacent to Wickes)	<p>Paving installation works.</p> <p>Kerb installation works.</p> <p>Concrete pouring for footpath foundations.</p> <p>Installation of streetlight ducting network.</p> <p>Installation of street light foundations.</p>	

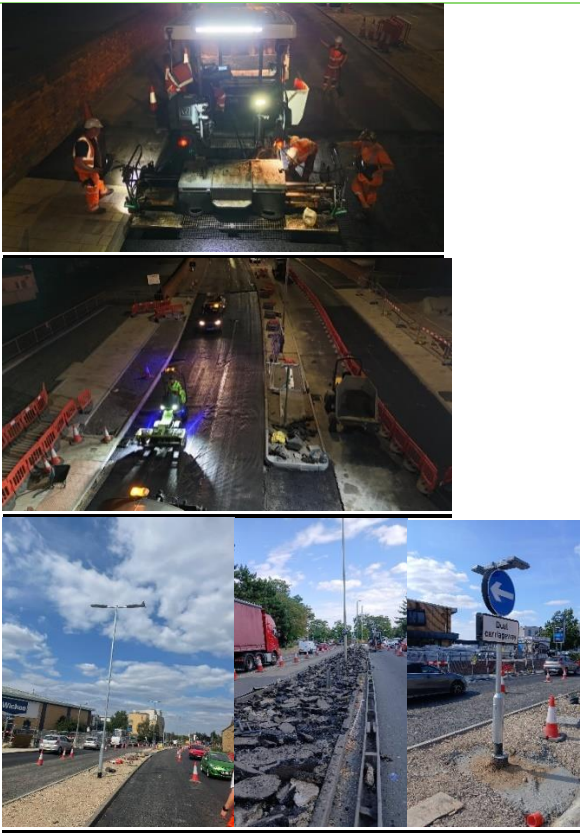
	<p>Monarchs Way</p> <p>Resurfacing works (Saturday and Sunday Night).</p> <p>Site clearance works.</p> <p>Installation of new streetlights.</p> <p>Installation of new road signage.</p>	
<p><u>Week ending 15 August</u></p>	<p>Eleanor Cross Monument to Eleanor Cross Road</p> <p>Construction of new splitter island at KFC.</p> <p>New footpath construction and installation of binder asphalt course.</p> <p>Ducting and foundation works.</p> <p>Footpath concrete foundation at monument area.</p>	

Eleanor Cross Monument to Park Lane

Kerb installation works.

Paving works.

Installation of utility and drainage chamber covers.

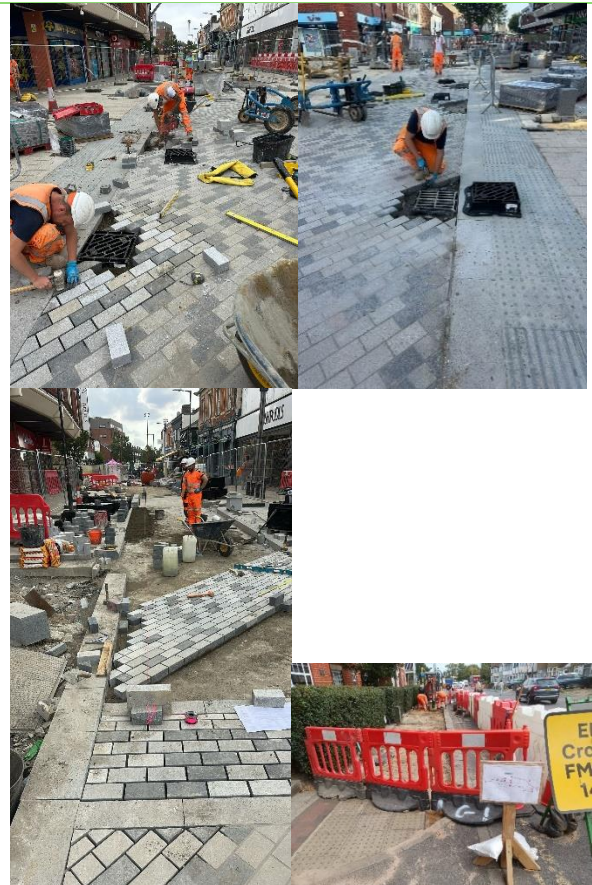

Park Lane to northern end of the High Street (adjacent to Wickes)


Paving installation works.



Kerb installation works.



Concrete pours to footpath foundations.

Installation of streetlight ducting network.

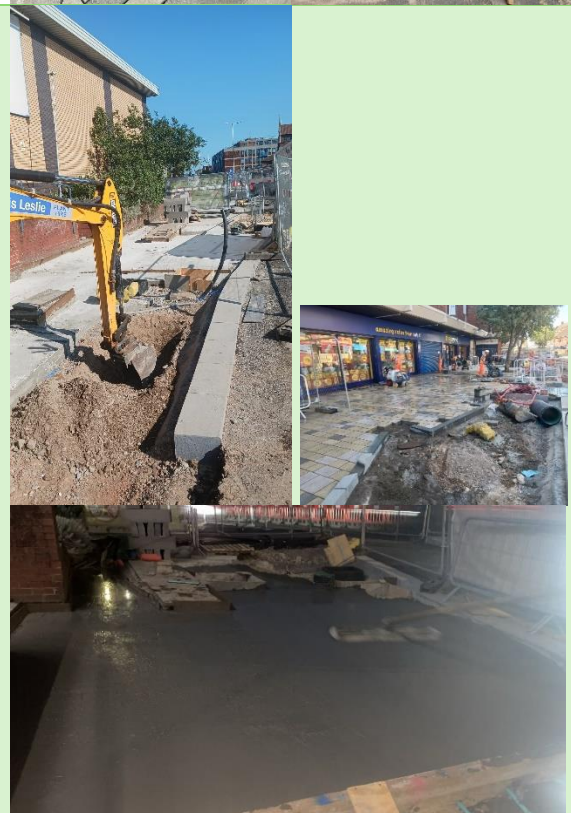Installation of street light foundations.

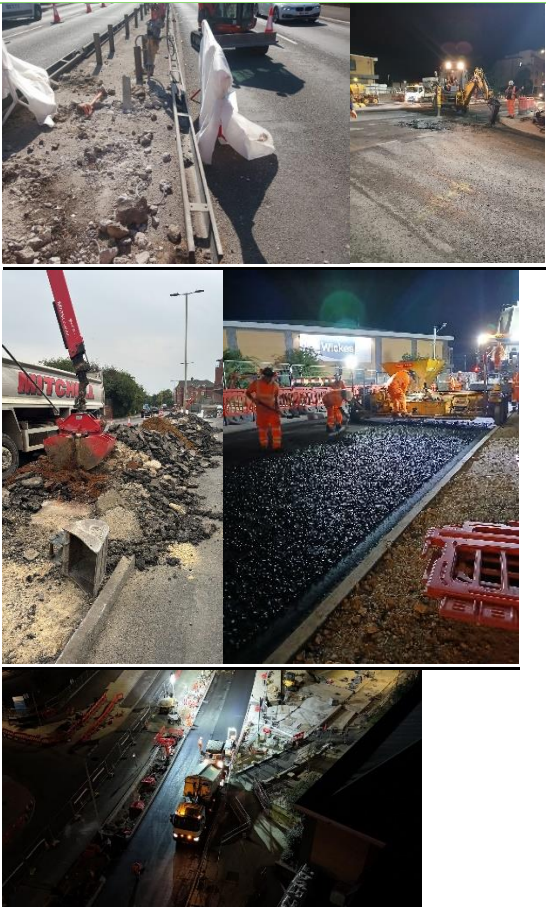

	<p>Monarchs Way</p> <p>Resurfacing works (Saturday and Sunday Night).</p> <p>Site clearance works to central reservation.</p> <p>Installation of new street light ducting.</p>	
	<p>Park Lane</p> <p>Site clearance to footpath.</p> <p>Preparation of Concrete footpath foundations.</p> <p>Utility trial holes.</p>	
<p><u>Week ending 8 August</u></p>	<p>Eleanor Cross Monument to Eleanor Cross Road</p>	<p>Kerb installation works.</p> <p>Relaying of York stone pavement.</p> <p>Street lighting and Monument lighting duct network installation.</p> 

	<p>Eleanor Cross Monument to Park Lane</p>	<p>Kerb installation works.</p> <p>Paving works.</p> <p>Concrete pouring for footpath foundations.</p>	
	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Paving installation works.</p> <p>Kerb installation works.</p> <p>Concrete pours to footpath foundations.</p> <p>Installation of Traffic signal Ducting network.</p> <p>Installation of street light ducting network.</p>	

	Monarchs Way	<p>Drainage works.</p> <p>Ducting network installation.</p> <p>Traffic signal socket and foundation installation.</p> <p>New Kerb alignment installation.</p> <p>Resurfacing works (Saturday and Sunday Night).</p>	
<u>Week ending 1 August</u>	Eleanor Cross Monument to Eleanor Cross Road	<p>Excavation and infill of rain garden and planter areas.</p> <p>Kerb and paving installation works.</p> <p>Street lighting and Monument lighting duct network installation.</p>	
	Eleanor Cross Monument to Park Lane	<p>Kerb installation works.</p> <p>Paving works.</p> <p>Concrete Pours to footpath foundations.</p>	

	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Paving installation works.</p> <p>Kerb installation works.</p> <p>Concrete pours to footpath foundations.</p> <p>Installation of Traffic signal Ducting network.</p> <p>Installation of street light ducting network.</p>	
	<p>Monarchs Way</p>	<p>Site clearance.</p> <p>Drainage works.</p> <p>Ducting work across Monarch way.</p> <p>New Kerb alignment installation.</p> <p>Resurfacing works (Saturday and Sunday Night).</p>	

**Week
ending 25
July**

**Eleanor Cross
Monument to
Eleanor Cross
Road**

Excavation and
preparation for
footpath bays.

Kerb and paving
installation works.

Concrete pours to
footpath
foundation.

Constuction of rain
garden and planter
areas.




**Eleanor Cross
Monument to
Park Lane**


Kerb installation
works.



Paving works.



Concrete Pours to
road foundation.

Concrete Pours to
footpath
foundations.

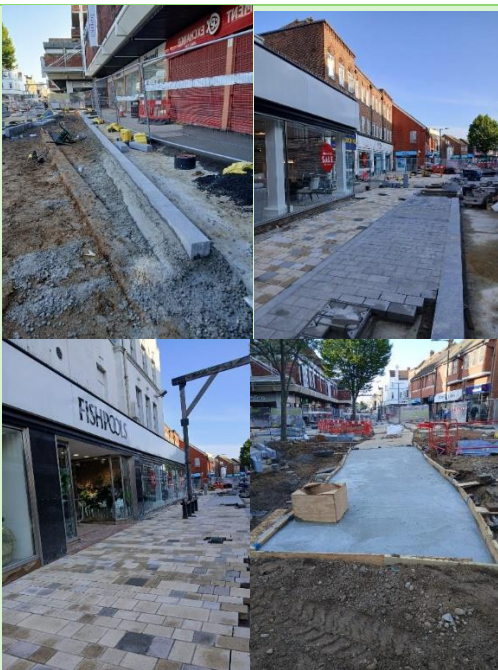

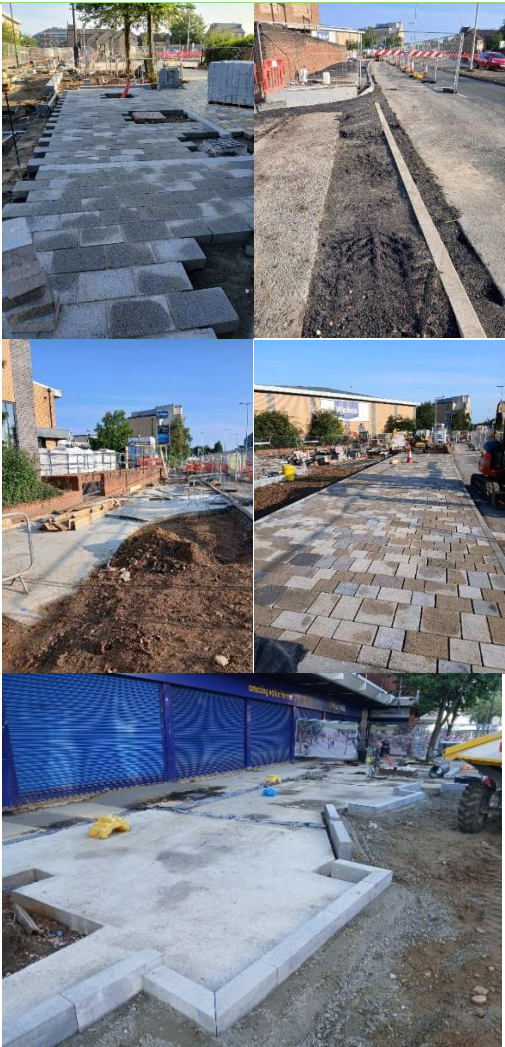	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Paving installation works.</p> <p>Kerb installation works.</p> <p>Concrete pours to footpath foundations.</p> <p>Installation of traffic signal ducting network.</p> <p>Installation of traffic signal pole foundations.</p> <p>Installation of streetlight ducting network.</p> <p>Asphalt to footpath.</p> <p>Tactile installation.</p> <p>Drainage works.</p>	
	<p>Stanhope Road</p>	<p>Removal of fencing.</p> <p>Asphalt works to road.</p>	

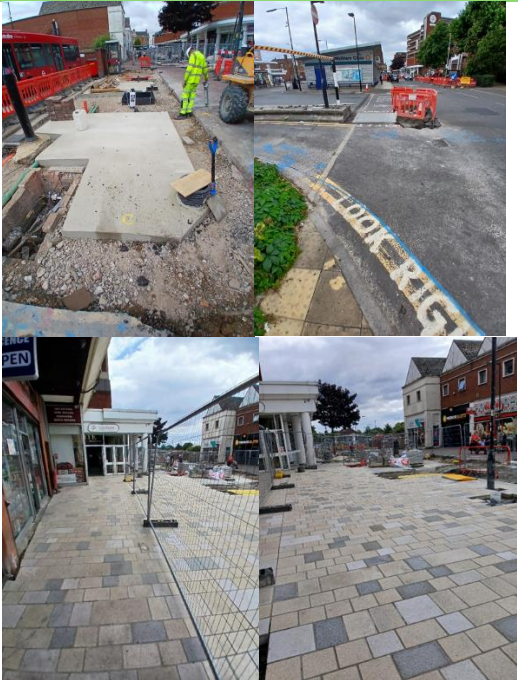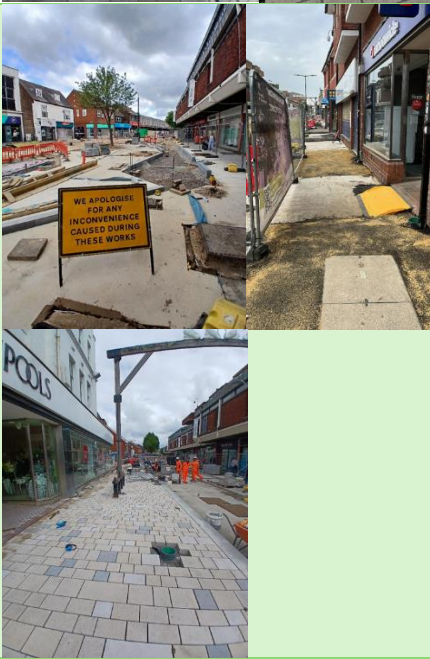
<p><u>Week ending 18 July</u></p>	<p>Eleanor Cross Monument to Eleanor Cross Road</p>	<p>Tree cell works (Excavation, fill and build up).</p> <p>Excavation and preparation for footpath bays at bus station.</p> <p>Kerb and paving installation in front of shopping centre.</p>	
	<p>Eleanor Cross Monument to Park Lane</p>	<p>Kerb installation works.</p> <p>Low Impact Development (LID) setting and paving block installation.</p> <p>Addition of temporary ramp to the library after concrete paving foundation laid.</p>	

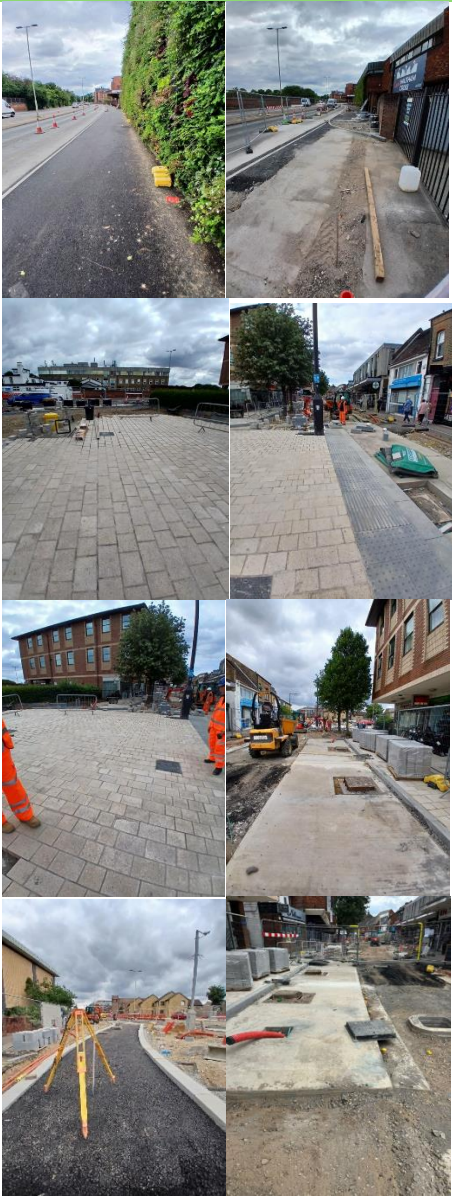	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Paving installation.</p> <p>Asphalt laid to footpath on Monarchs Way.</p> <p>Surface bonding layer added to High Street and Monarchs Way.</p> <p>Kerb installation works.</p>	
	<p>Stanhope Road</p>	<p>Top soil addition to verges.</p>	

**Week
ending 11
July**


**Eleanor Cross
Monument to
Eleanor Cross
Road**

Site clearance.
Drainage works.
Tree cell build up
finishing works.
Excavation and
preparation for
footpath bays.
Kerb and paving
installation works.

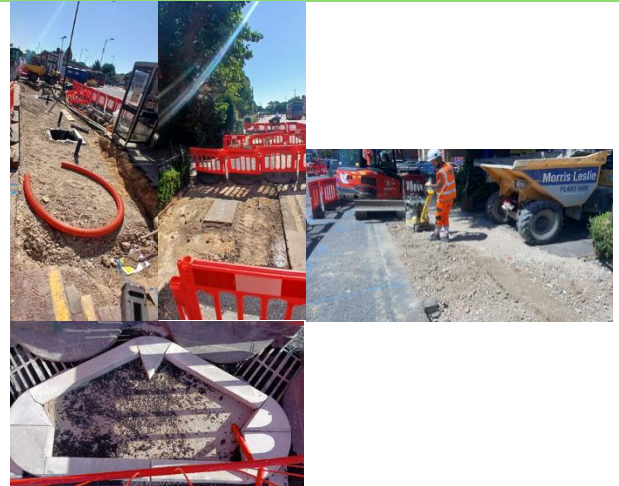



**Eleanor Cross
Monument to
Park Lane**

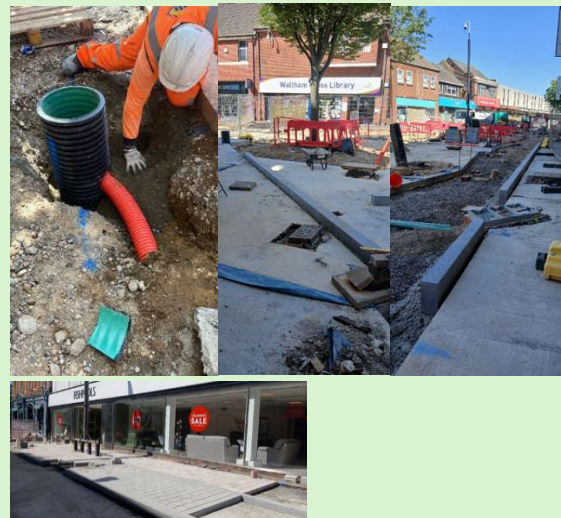Kerb installation.
Streetlight ducting
and sleeves
installation.
Paving works.





	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Paving installation.</p> <p>Preparation for binder on Monarch's Way Footpath.</p> <p>Preparation and pouring footpath concrete bays.</p> <p>Drainage works.</p>	
	<p>Stanhope Road</p>	<p>Planter finishing.</p> <p>Drainage works.</p>	
<p><u>Week ending 4 July</u></p>	<p>Eleanor Cross Monument to Eleanor Cross Road</p>	<p>Site clearance.</p> <p>Drainage works.</p> <p>Tree cell works (Excavation, fill and build up).</p> <p>Excavation and preparation for footpath bays at bus station.</p> <p>Kerb and paving installation in front of shopping centre.</p>	

	<p>Eleanor Cross Monument to Park Lane</p>	<p>Planter finishing works.</p> <p>Excavation and preparation for footpath bays.</p> <p>Kerb installation works.</p> <p>Lid setting and paving block installation.</p> <p>Trial hole works.</p>	
	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Excavation preparation for asphalt on footpath on Monarch's Way.</p> <p>Finishing road trim works to ahead of asphalt pouring on High Street.</p> <p>Paving installation works.</p> <p>Drainage works.</p> <p>Asphalt laid to footpath on Monarchs Way.</p> <p>Traffic signal box and duct installation.</p> <p>Kerb installation works.</p> <p>Tree cell works.</p> <p>Trial hole works.</p>	

	Stanhope Road	<p>Planter finishing works.</p> <p>Drainage works.</p>		
<u>Week ending 27 June</u>	Eleanor Cross Monument to Eleanor Cross Road	<p>Site clearance works.</p> <p>Tree cell excavations works and installation.</p> <p>Work on street lighting and ducting installation.</p> <p>Drainage works.</p> <p>Paving and kerb installation</p>		
	Eleanor Cross Monument to Park Lane	<p>Site clearance and excavation to formation</p> <p>Planter excavation works and material fill.</p> <p>Excavation and preparation for footpath bays at shop fronts.</p> <p>BT Chamber adjustment and repair works.</p>		

	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Tree cell excavation and fill works (Material fill and build up).</p> <p>Excavation and prep for road formation and kerbs.</p> <p>Kerb and paving installation works.</p> <p>Excavation and preparation for footpath bays at shop fronts.</p> <p>Footpath clearance at Monarchs Way.</p> <p>Kerb installation on Monarchs Way.</p> <p>Installing traffic signal ducting and sleeves.</p> <p>Excavation ahead of footpath formation at Monarchs Way.</p>	
	<p>Stanhope Road</p>	<p>Planter excavation works (Material fill and build up).</p>	
<p><u>Week ending 20 June</u></p>	<p>Eleanor Cross Monument to Eleanor Cross Road</p>	<p>Site clearance works.</p> <p>Kerb line preparation and installation.</p> <p>Excavation for tree cells.</p>	

		<p>Excavation and preparation for concrete bays and concrete pouring at bus shelter.</p> <p>Paving installed at footpath at bus shelter.</p>	
	<p>Eleanor Cross Monument to Park Lane</p>	<p>Excavation and preparation for footpath bays at shop fronts on east wing.</p> <p>Planter works.</p> <p>Excavating for planters and rain gardens.</p>	
	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Tree cell works.</p> <p>Excavation and preparation for road formation. Setting lids on chambers around site.</p> <p>Kerb and paving installation works.</p> <p>Excavation and preparation for footpath bays at shop fronts.</p> <p>Site clearance to footpath at Monarchs Way.</p>	

		<p>Kerb installation on Monarchs Way.</p> <p>Breaking out kerbs and existing asphalt at footpath on Monarchs Way.</p> <p>Installation of traffic signal ducting and sleeves.</p>	
	Stanhope Road	<p>Drainage works.</p> <p>Planter finishing works.</p> <p>Start of new planter excavation and preparation work.</p>	
<u>Week ending 13 June</u>	Eleanor Cross Monument to Eleanor Cross Road	<p>Continued site clearance at bus station.</p> <p>Installing electric ducting and sleeves.</p> <p>Kerb and paving installation.</p> <p>Kerb installation at bus station.</p> <p>Footpath bay preparation and concrete pouring.</p> <p>Drainage works.</p>	

Eleanor Cross Monument to Park Lane

Concrete pouring for footpath and parking bays.

Excavation for planters.

Tree cell finishing works.



Park Lane to northern end of the High Street (adjacent to Wickes)

Excavation prep for footpath bays at Monarchs Way.

Concrete pouring in footpath bays.

Excavation for kerbs and road to be asphalted.

Street lighting duct installation.

Continued kerb and paving installation near underpass/Wickes.

Planter works.

Road planning works for new kerb line on Monarchs Way.





Stanhope Road

Demolition works for planter installation

Material fill into planter area.

Painting of underpass wall.



Week ending 6 June

Eleanor Cross Monument to Eleanor Cross Road

Site clearance by Bus Station.

Installation of electric ducting and sleeves.

Drainage works.

Kerb and tactile paving installation.




**Eleanor Cross
Monument to
Park Lane**

Excavation and
preparation for
installation of
footpath and
parking bays.

Concrete pouring
on footpath and
parking bays.

Finishing works for
chamber lids.

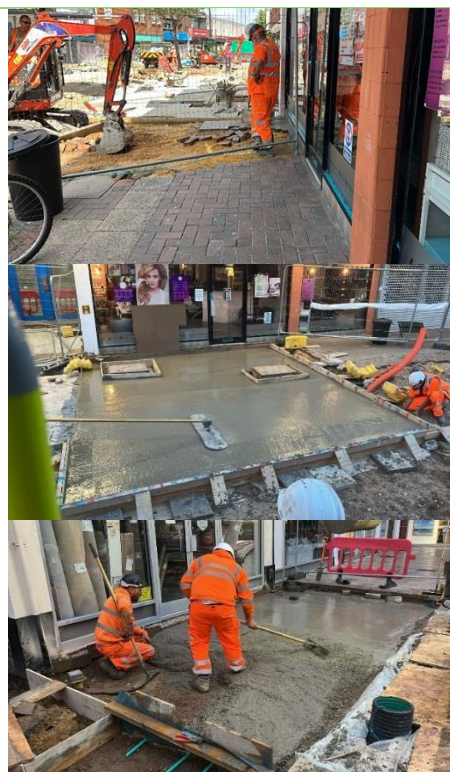

**Park Lane to
northern end of
the High Street
(adjacent to
Wickes)**

Excavation for
footpath bays.

Pouring concrete in
footpath bays.

Demolition of
underpass walls
completed.


Monarchs Way
footpath site
clearance.

Street lighting
ducting installation.

Installation of
paving near
mobility shop.



Planter works.

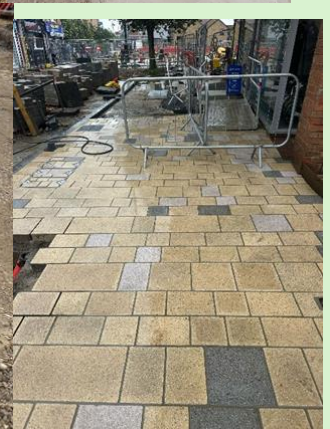


Preparation to
excavate road for
asphalt installation.






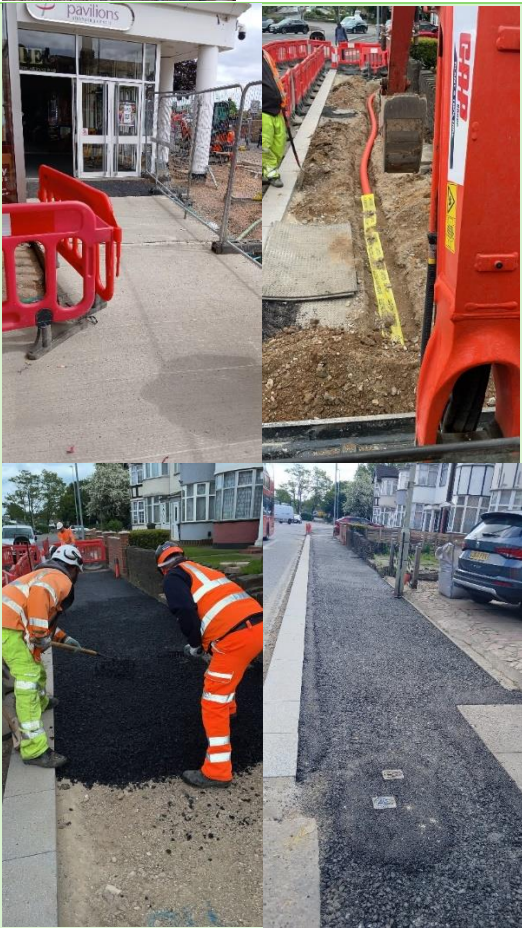
	Stanhope Road	<p>Finishing works for chamber lids.</p> <p>Excavation for planters.</p> <p>Laying binder to footpath.</p> <p>Kerb installations.</p>	
<u>Week ending 30 May</u>	Eleanor Cross Monument to Eleanor Cross Road	<p>Started site clearance at bus station.</p> <p>Continued excavation and preparation for footpath bays.</p> <p>Concrete pouring in footpath bays.</p> <p>Virgin Media chamber adjustment works.</p> <p>Drainage works.</p> <p>Street lighting cable installation.</p>	

	<p>Eleanor Cross Monument to Park Lane</p>	<p>Excavation digs and preparation for footpath bays at Fishpools and shopping centre.</p> <p>Concrete pouring in footpath and parking bays.</p> <p>Completion of tree cell works.</p> <p>Paving and kerb works continued between Fishpools and costa.</p>	
	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Tree cell works.</p> <p>Excavation preparation for footpath bays.</p> <p>Concrete pouring in footpath bays.</p> <p>Trial holes for subway wall demolition works.</p> <p>Subway wall demolition works.</p> <p>Monarchs Way footpath site clearance.</p> <p>Cable installation for street lighting installation.</p>	

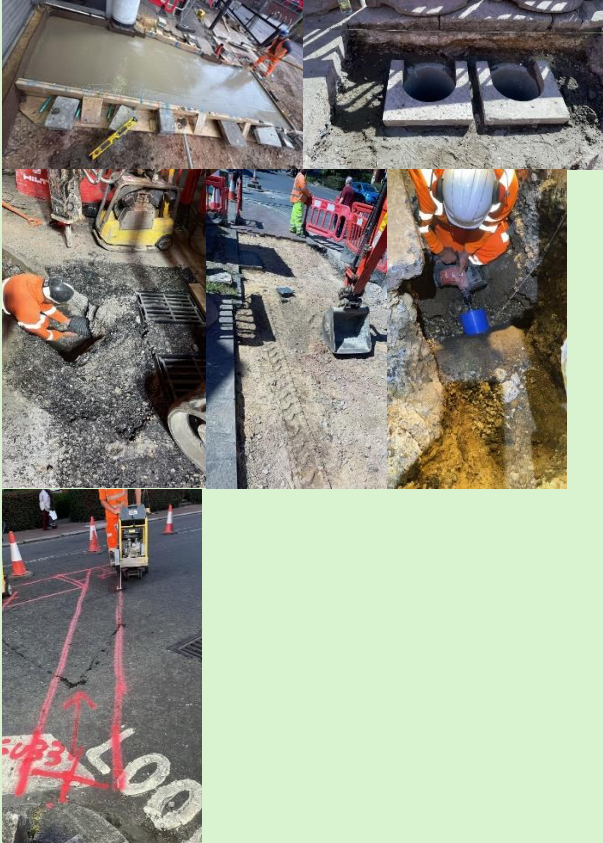	Stanhope Road	Continuation of paving works.	
<u>Week ending 23 May</u>	Eleanor Cross Monument to Eleanor Cross Road	<p>Installation of streetlight cables.</p> <p>Grading and preparation for binder course.</p> <p>Continued work on footways.</p> <p>Break out and excavation drainage works for gullies</p> <p>installation and connection to mains in the road.</p> <p>UKPN preparation works.</p>	
	Eleanor Cross Monument to Park Lane	<p>Laying paving in road section between Fishpools and Costa Coffee.</p> <p>Concrete pouring on footway bays.</p> <p>Installation of subsoil to tree cells.</p>	

	Park Lane to northern end of the High Street (adjacent to Wickes)	<p>Concrete pouring on road and footway bays.</p> <p>Temporary surfacing in front of the Mobility Shop.</p>	
	Stanhope Road	<p>Preparation for footpath bay installation</p> <p>Concrete pouring on footpath bay.</p> <p>Start of kerb edging installation and paving works on the southside.</p>	
<u>Week ending 16 May</u>	Eleanor Cross Monument to Eleanor Cross Road	<p>Excavation and preparation for footpath bays around the shopping centre.</p> <p>Pouring concrete in footpath bays.</p> <p>Break out and excavation of ground for drainage and gullies installation, and connection to the main run in the road.</p> <p>UKPN (UK Power Network) preparation works.</p>	

	<p>Eleanor Cross Monument to Park Lane</p>	<p>Paving work between Fishpools and Costa Coffee.</p> <p>Excavation and preparation for footpath bays in front of Bon Marche, CEX and shopping centre doors.</p> <p>Concrete pouring in footpath bays in front of Bon Marche, CEX and shopping centre doors.</p> <p>Site clearance by Fishpools.</p>	
	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Drainage works (gullies installation and connections).</p> <p>Excavation and preparation for road and footpath bays.</p> <p>Pouring concrete at road and footpath bays in front of La Valle.</p> <p>Continued underpass demolition works.</p>	 <div data-bbox="863 1704 1465 1736"><div>13 May 2025 15:26:11 132A High St, Waltham Cross EN8 7AP, UK</div><div>15 May 2025 17:33:44 143 High St, Waltham Cross, London EN8 7AP, UK</div></div>

	<p>Stanhope Road</p> <p>Preparation for footpath bay installation.</p> <p>Concrete pouring at footpath bay.</p> <p>Kerb and edging installation and paving works.</p>	
<p><u>Week ending 9 May</u></p>	<p>Eleanor Cross Monument to Eleanor Cross Road</p> <p>Preparation for footpath bays at pharmacy and shopping centre.</p> <p>Removal of bollards at fire brigade gate for footpath bay preparation.</p> <p>Excavation for streetlight cables along footpath on southside.</p> <p>Preparation of footpath for asphalt binder laying.</p> <p>Drainage excavations for gullies to be installed on the road.</p>	




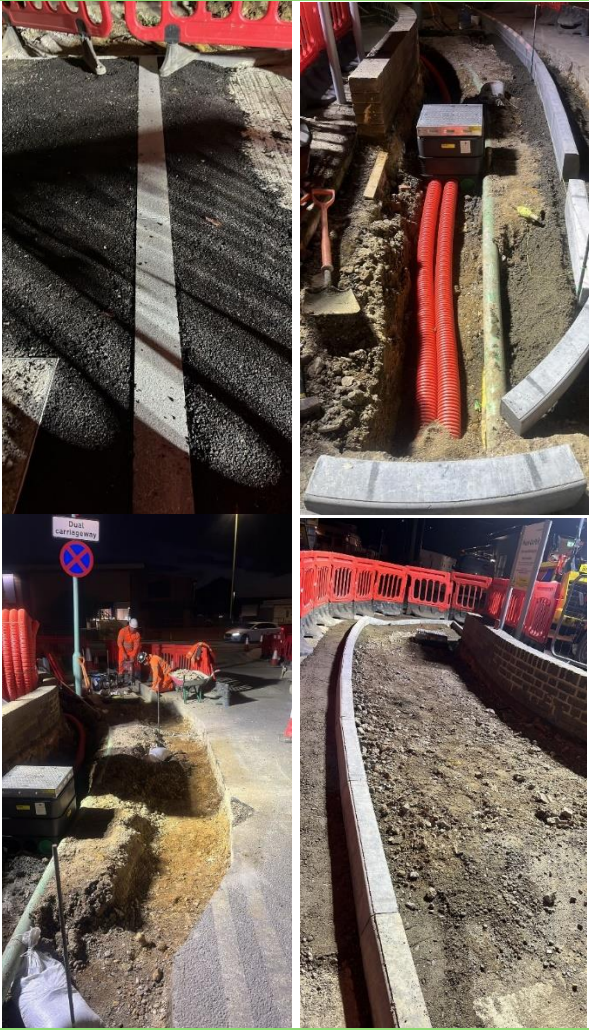
Eleanor Cross Monument to Park Lane

Installation of edgings, laying of paving and grouting in east wing market area and in front of Costa Coffee.

Excavation and preparation for footpath bays in front of Bon Marche.

Pouring of concrete in footpath bays in front of Bon Marche.



	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Drainage works (installation of gullies).</p> <p>Excavation and preparation for footpath bays in front of La Valle, in addition to concrete pouring on the footpath.</p> <p>Continued underpass demolition works.</p>	
	<p>Stanhope road</p>	<p>Excavation for traffic signal boxes, ducting, signpost sleeves and kerb installation near NHS entrance.</p> <p>Temporary tarmac laid on Northside near substation to open access for pedestrians.</p>	

**Week
ending 2
May**

Stanhope Road

South of Junction

Pedestrian walkways altered.

Excavation and Subbase laid for Footpath construction.

Footpath concrete paving foundations poured.

North of Junction

Clearance of existing footpath and kerb line.

Excavation and Subbase laid for Footpath construction.

New kerb line installed.

Concrete paving foundations poured.



**Park Lane to
northern end of
the High Street
(adjacent to
Wickes)**

Excavation for kerb braces, parking bays and footpath concrete foundations.

Concrete pours for footpath bays and kerb braces.


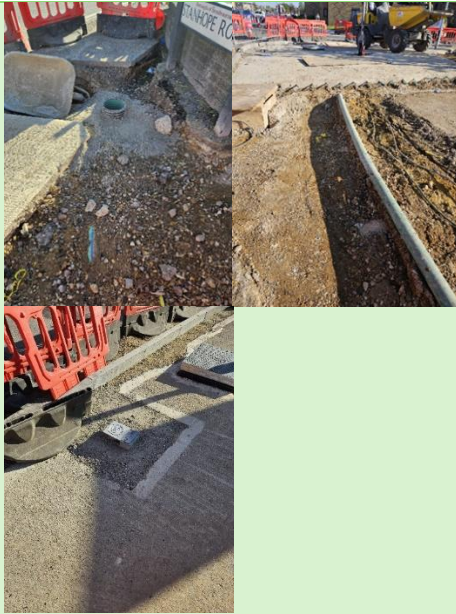
Drainage works.


Demolition works to existing subway wall.

New street light network cables installed.






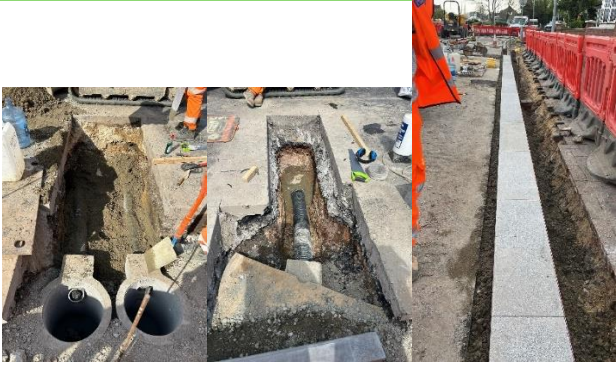


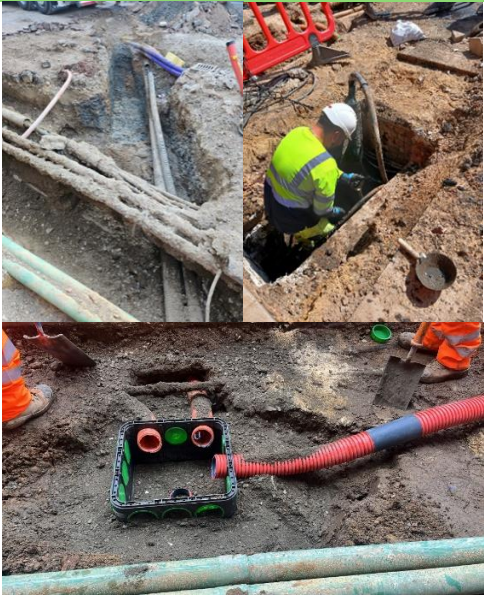
		Continued work on high voltage cable diversion and reinstatement.		
	Eleanor Cross Monument to Park Lane	<p>Footpath paving concrete foundations poured in front of Savers doorway and shop front.</p> <p>Block Paving installed to Market area.</p> <p>New street lighting network cable installed.</p> <p>Removal of existing Street lights.</p>	  	
	Eleanor Cross Monument to Eleanor Cross Road	<p>Concrete paving foundations poured in front of shop fronts and doorways at Pavilions Mobile Tech and Handerson's news agents.</p> <p>Excavation and concrete paving foundation works progressed in front of Pavilions shopping centre and in front on Timpson.</p>	 	

		Removal of existing streetlights.	
	Eleanor Cross Road	<p>Traffic management layout change.</p> <p>Footpath temporarily reopened.</p> <p>Existing footpath excavated and subbase laid.</p> <p>Clearance of existing block paving.</p> <p>Utility covers set to correct levels.</p>	
<u>Week ending 25 April</u>	Stanhope Road	<p>Demolition of Existing underpass walls.</p> <p>Subbase laid for Footpath construction.</p> <p>Removal of existing streetlighting.</p> <p>Installation of new street lighting cables.</p> <p>Installation of traffic signal control sockets and foundations.</p> <p>Removal of existing kerb line.</p>	

	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Excavation for kerb braces, parking bays and footpath concrete foundations.</p> <p>Concrete pours for footpath bays and kerb braces.</p> <p>Drainage works.</p> <p>Demolition works to existing subway wall.</p> <p>New street light network ducts installed.</p> <p>Continued excavation for high voltage cable diversion.</p> <p>High voltage cable diversion.</p> <p>Lowering of utility chambers.</p>	
	<p>Eleanor Cross Monument to Park Lane</p>	<p>Work progressed further along shop frontages.</p> <p>Continued excavation to Footpath in front of Costa coffee.</p> <p>Concrete foundations poured.</p> <p>Excavation to Footpath in front of Savers Phase 1 and concrete foundations poured.</p>	

		<p>New Street lighting network ducts installed.</p> <p>Removal of existing streetlights.</p>	
	Eleanor Cross Monument to Eleanor Cross Road	<p>Works in front of shop frontages progressed to new sections.</p> <p>Continued work on excavation of footpath and parking bays, subbase laid, and concrete foundations pouring.</p> <p>Removal of existing Street lights.</p>	
	Eleanor Cross Road	<p>Existing footpath excavated and subbase laid.</p> <p>Tactile crossing installation.</p> <p>Asphalt base course laid.</p> <p>Streetlight network ducting installed.</p> <p>Removal of old street furniture.</p>	
<u>Week ending 18 April</u>	Stanhope Road	<p>Concrete footpath foundations prepped and poured.</p> <p>Traffic signal ducting installed.</p> <p>Demolition of existing subway parapet wall.</p>	

		<p>Site clearance of existing kerb line.</p> <p>Trial holes along existing footpath.</p>	
	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Excavation for kerb braces, parking bays and footpath concrete foundations.</p> <p>Concrete pours for footpath bays and kerb braces.</p> <p>Drainage works.</p> <p>Demolition works to existing subway wall</p> <p>New street light network ducts installed.</p> <p>Trial Holes in preparation of high voltage cable diversion.</p>	
	<p>Eleanor Cross Monument to Park Lane</p>	<p>Work area progressed to shop frontages.</p> <p>Excavation of footpath in front of Costa Coffee.</p> <p>Concrete foundations poured.</p> <p>New street lighting network ducts installed.</p>	

	Eleanor Cross Monument to Eleanor Cross Road	<p>Works progressed to shop frontages.</p> <p>Excavation of footpath and parking bays to formation and subbase laid.</p>	
	Eleanor Cross Road	<p>New 80 metre Kerb line installed.</p> <p>New street light network ducting installed.</p> <p>New road drainage gullies installed and connected to live main.</p> <p>Footpath widening excavated and subbase laid.</p> <p>Existing footpath excavated and subbase laid.</p>	 
<u>Week ending 11 April</u>	Stanhope Rd	<p>Concrete pouring footpath foundations.</p> <p>Cable installation for new traffic lights.</p> <p>Site clearance of infilled underpass.</p>	 

Park Lane to northern end of the High Street (adjacent to Wickes)

Excavation for parking bays, kerb braces and footpath concrete foundations (concrete pouring was also carried out for the last two activities).

Continued drainage works and excavation for tree planting areas.










Eleanor Cross Monument to Park Lane

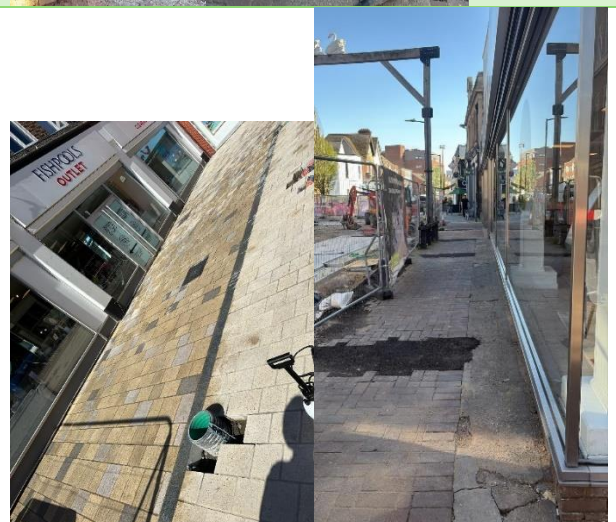

Investigative work in front of Fishpools with trial holes.

Trials holes were also drilled to check for drainage.





New paved area in front of Fishpools was reopened.



	Eleanor Cross Monument to Eleanor Cross Road	<p>Pouring of concrete slab for new parking and road bays.</p> <p>Continued excavation and development of the new road, and alignment work for the new kerb.</p>	 
	Eleanor Cross Road	<p>Work in this section is being approached in two phases.</p> <p>For the first phase, several activities were undertaken this week including relocation of temporary traffic lights, start of drainage works, clearance of existing kerb lines and installation of new kerb lines.</p>	 
<u>Week ending 4 April</u>	Stanhope Road	<p>Excavation of existing footpath and installation of new concrete footpath foundation.</p>	 

	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Excavation for kerb braces, parking bays and footpath concrete foundations.</p> <p>Concrete pouring for footpath bays and kerb braces.</p> <p>Street lighting removal and installation of temporary solar powered street lighting.</p> <p>Continuation of drainage works.</p>	
	<p>Eleanor Cross Monument to Park Lane</p>	<p>Removal of street lighting and installation of temporary solar powered lighting.</p> <p>Trial hole drilling to check for existing drainage.</p> <p>Application of protective sealant to paving.</p>	

	Eleanor Cross Monument to Eleanor Cross Road	Concrete slab pouring for parking and road bays, and continued excavation and development of the new road.		
	Eleanor Cross Road	<p>Installation of traffic management. Removal of street lighting, furniture and splitter island.</p> <p>Following removal of the splitter island, Asphalt was reinstated.</p>	 	
<u>Week ending 28 March</u>	Eleanor Cross Monument to Eleanor Cross Road	Road formation work, installation of streetlight cables and sleeves and concrete slab		


		pouring on footpath bays.	
	Eleanor Cross Monument to Park Lane	<p>Finalised grouting and completed paving and kerbing in front of Fishpools.</p> <p>Excavation and installation of tree cells in front of the shopping centre.</p>	   

**Park Lane to
northern end of
the High Street
(adjacent to
Wickes)**

Excavation for tree
cell installation,
backfilling of
diverted electricity
cable, excavation
for kerb braces,
parking bays and
footpath concrete
foundations.

Concrete was
poured on installed
footpath bays and
braces.

Drainage works
continued and a
temporary footpath
was set up outside
One Beyond.

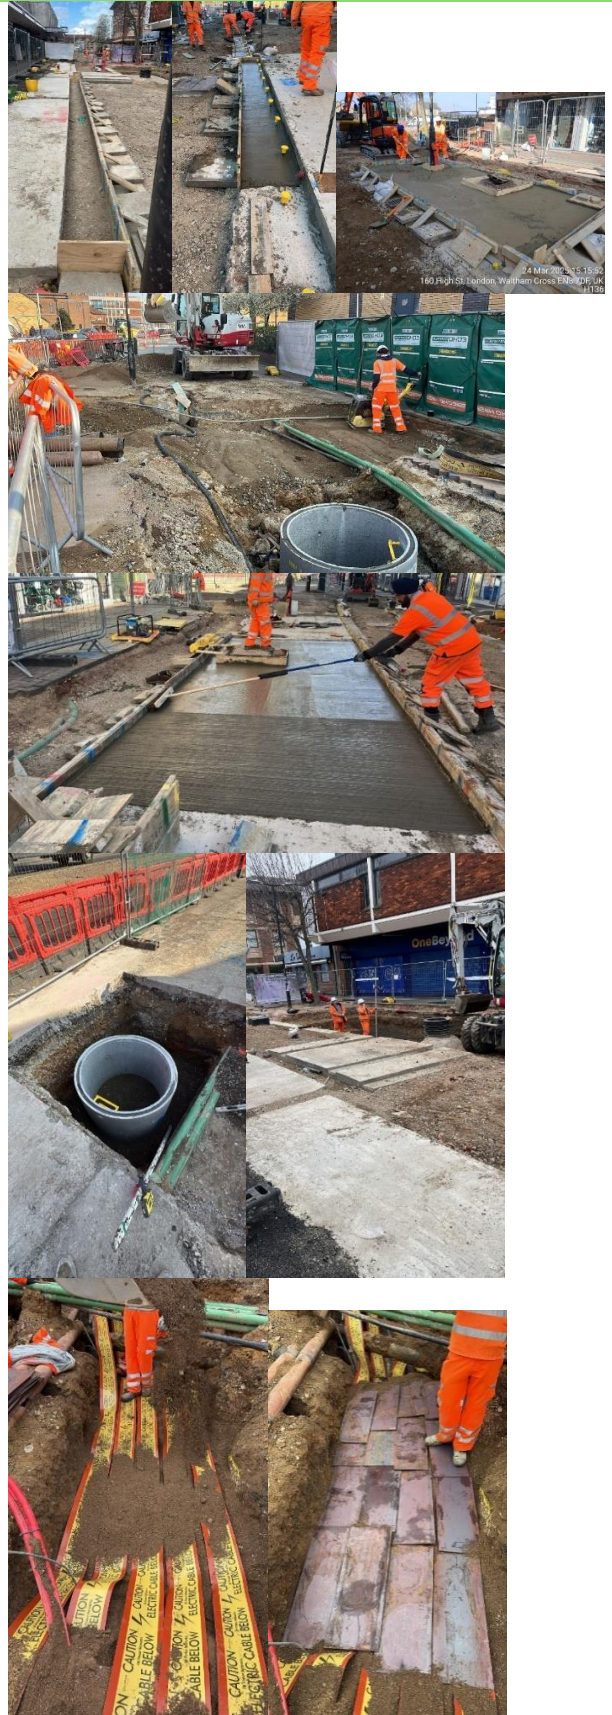

	Stanhope Road	Excavation and installation of new traffic light cables and kerbs	   
<u>Week ending 21 March</u>	Eleanor Cross Monument to Eleanor Cross Road	<p>Removal of existing paving, and excavation for new road and kerb.</p> <p>Excavation work for new parking bays.</p>	
	Eleanor Cross Monument to Park Lane	<p>Paving installation in front of Fishpools.</p> <p>Existing electricity utility diversion work.</p> <p>Excavation for new tree pits and rain garden drainage.</p>	



**Park Lane to
northern end of
the High Street
(adjacent to
Wickes)**

Continued
drainage works
and excavation for
kerb braces, new
road alignment,
parking bays and
footpath concrete
foundations.

Excavation for new
tree pits and rain
garden drainage.

Diversion of
existing electricity
utility.
Installation of new
street lighting
power cables.



	<p>Stanhope Road</p>	<p>Nighttime work for drainage installation and new traffic signal cabling installation.</p>	
<p><u>Week ending 14 March</u></p>	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Continuation of drainage works, excavation for kerbs, parking bays and rain gardens.</p> <p>Installation of concrete protection around utilities.</p>	
		<p>Concrete pouring for footpath foundation, and continued work on placement and compaction of road stone.</p> <p>Continued excavation for rain garden.</p>	

Stanhope Road

New paving cleaned and protective sealant installed.

Work fencing was removed and the new pedestrian paving on the northern side of the junction was opened.

Preparation on the opposite side of the road for drainage and kerb works next week.



Eleanor Cross Monument to Park Lane

Concrete pour on footpath bays, drainage works and installation of new cables.

Preparation works in front of Fishpools to begin work on kerbs,



		edgings and block paving next week.	
		Continued excavation for electricity cable diversion and excavation for new planter area.	
	Eleanor Cross Monument to Eleanor Cross Road	Drainage works (saddle connections to carrier drainage pipe). Site clearance in preparation for more drainage work next week.	  
<u>Week ending 7 March</u>	Stanhope Road	Continued installation of new paving.	



Park Lane to northern end of the High Street (adjacent to Wickes)

Workers have started to excavate for the new 'rain gardens'.



Continuation of work on the underpass with stone infill completed, and continued demolition of existing walls.






		Existing utility cables lowered to enable road construction. Laying of road stone.	
	Eleanor Cross Monument to Park Lane	Additional pedestrian crossover points temporarily installed	
		Excavation to divert high voltage electricity cable	
		Cable ducting work to new street lighting installation.	




		Continued work on concrete pouring on road and footpath bays, and excavation for planter area has started.	
	Eleanor Cross Monument to Eleanor Cross Road	Continuation of drainage works and trial excavations to locate existing utility pipes	
<u>Week ending 28 February</u>	Northern end of the High Street (new pedestrian crossings)	Continuation of paving slab installation at the new crossing point in Stanhope Road	
	Northern end of the High Street (underpass)	Work has continued to backfill the now decommissioned underpass at Monarchs Way	

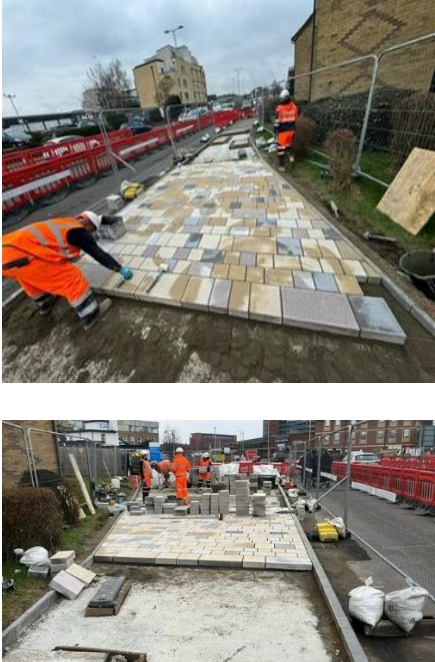


	Park Lane to northern end of the High Street (adjacent to Wickes)	Continuation of work to lower existing utility ducts to accommodate new road surface.	
	Eleanor Cross Monument to Park Lane	Concrete started to be poured along the High Street to serve as the new road foundation. Preparation work has continued to install new paving outside Fishpools.	 
<u>Week Ending 21 February</u>	Stanhope Road	Continued work on new paving installation, including the addition of tactile paving.	






	Park Lane to northern end of the High Street (adjacent to Wickes)	Work on breaking down the ramps that used to serve the former underpass has continue alongside backfilling to bring the ramp up to street level.		
	Park Lane to northern end of the High Street (adjacent to Wickes)	Lowering of existing utility ducts to accommodate new road surface.		
	Eleanor Cross Monument to Park Lane	Old paving removed from outside Fishpools. Concrete bays have been installed outside the shop, these will support the new foundation and paving.	 	




<p><u>Week Ending 14 February</u></p>	<p>Stanhope Road</p>	<p>New paving slabs installed at the new pedestrian crossing.</p>	
	<p>northern end of the High Street (adjacent to Wickes)</p>	<p>Infilling of former underpass ramp section with stones. This is being done to bring this section up street level.</p>	
	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Continued excavation work for new drainage runs. This is progressing well with 90% of the drainage now installed.</p>	

	Eleanor Cross Monument to Park Lane	Concrete base for the new road was poured and levelled. These new concrete bays will serve as the foundation for the new paving slabs.	
<u>Week Ending 7 February</u>	Stanhope Road	Concrete foundations for the new pedestrian crossing laid. Traffic light bases installed and tested.	
	Park Lane to northern end of the High Street (adjacent to Wickes)	Continued excavation for installation of drainage runs along this location.	
	Eleanor Cross Monument to Park Lane	Installation of shutter frames on the ground to support the paving's concrete foundations.	

<p><u>Week Ending 31 January</u></p>	<p>Stanhope Road</p>	<p>Started to install concrete foundations to connect the new paving (also being installed) to the new pedestrian crossing.</p>	
	<p>Stanhope Road</p>	<p>Continued work to break up ramp that serviced the underpass. At the same time, drainage is also being installed next to the former underpass.</p>	
	<p>Park Lane to northern end of the High Street (adjacent to Wickes)</p>	<p>Continued excavation and installation of new drainage.</p>	
	<p>Eleanor Cross Monument to Park Lane</p>	<p>Continued work on the installation of concrete foundations for the new road. Ground levelling work in ongoing along with installation of bases for new lighting columns.</p>	

<u>Week Ending 24 January</u>	Stanhope Road	Decommissioned underpass has been filled with concrete. Work in progress to break up the concrete ramps that serviced the underpass ahead of filling these sections.	
	Stanhope Road	Kerbs have been installed in preparation for concrete pouring for new street foundations.	
	Stanhope Road	Ground preparation work to install the new pedestrian crossings has commenced.	
	Park Lane to northern end of the High Street (adjacent to Wickes)	Drainage installation	
	Eleanor Cross monument to Park Lane	Drainage work in this section has been completed. Concrete started being poured for foundation of the new road	


<u>Week Ending 17 January</u>	Stanhope Road	Work on filling underpass has commenced. This work took three days to complete.	  <p>14 Jan 2025 10:37:32 178A Stanhope Road Hertfordshire England</p>
Week ending 10 January	Stanhope Road	Wooden shutters installed in underpass to support concrete filling.	 <p>13 Dec 2024 11:21:41 39a King Edward Road Hertfordshire England</p>
	Park Lane to northern end of the High Street (adjacent to Wickes)	Start of planned drainage installation to go around existing utilities.	
	Eleanor Cross Road Monument to Park Lane	Excavation for new road foundation and streetlights as well as ducting to power new streetlights.	

2024				
Week ending 13 December	Monarchs Way	All road closure barriers were removed to facilitate traffic flow during the Christmas period when work in the town centre will be suspended.		
	Stanhope Road	Pipes and ducting installed at Monarchs Way underpass. Work commenced to install shutters that will retain the concrete which is to be poured in a few weeks.		
	Park Lane to Monarchs Way	Investigative work for existing utility duct that needs to be lowered in this area.		
	Eleanor Cross Road Monument to northern end of the High Street (adjacent to Wickes)	Digging to accommodate foundations of the new road commenced.		




	Eleanor Cross Road Monument to Park Lane	<p>Work to lower existing utility duct ahead of new pavement installation.</p> <p>Continuation of drainage installation.</p>	 
Week ending 6 December	Monarchs Way	Road works on Monarchs Way completed.	
	Stanhope Road	Preparation ahead of disconnection of electrical services in the underpass linking Stanhope Road with the High Street.	
	Park Lane to Monarchs Way	Removal of existing paving and setting out of new lines for proposed drainage locations.	
	Eleanor Cross Monument to Park Lane	Continued work to lower existing utility ducts, and work to start reducing the existing ground to the correct level for the new road.	





Week ending 29 November	Stanhope Road	Installation of new kerbs and bases for the new traffic lights.	
	Park Lane to Monarchs Way	Extension of fencing lines ahead of removal of existing pavement.	
	Monarchs Way	Drainage installation completed.	
	Northern end of the High Street	Section of drainage installation completed.	

	Near Queen Eleanor Monument Towards northern end of the High Street	Lowering of existing utility duct, and continued installation of drainage.		
	From Eleanor Cross Monument to Park Lane	Completion of gas main installation and backfilling, and removal of fencing from related section.		
Week ending 22 November	Stanhope Road	Excavations on the South Bound Carriageway to install the new kerb line and, excavations to allow the new traffic lights to be powered. In tandem, excavations have also commenced on the opposite side, (next to Wicks) for drainage and new kerbs.		

	Fishpools/High Street to Eleanor Cross Road	Preparation ahead of final connection of gas main, with testing and backfilling continuing in tandem.		
	Northern end of the High Street	Drainage installation planning to avoid existing utilities		
	From Eleanor Cross Monument to Park Lane	Continuation of drainage installation		
Week ending 15 November	Stanhope Road	Works on the new pedestrian crossing		

	From Fishpools/High Street to Eleanor Cross Road	Backfilling and testing of installed gas main		
	Northern end of High Street from Waltham Cross Bakery to Wicks	Vacuum excavation ahead of drainage installation.		
	From Eleanor Cross Monument to Park Lane	Excavation to reveal existing ducts and pipes, ahead of installation of new ones.	 14 Nov 2024 16:16:51 133 High Street Hertfordshire England	
Week ending 8 November	Monarchs Way	New Manhole was installed within the north bound carriage way		
	Stanhope Road	Installation of manholes. In addition, installation of ducts and pipes to feed new traffic light electricity continues.		

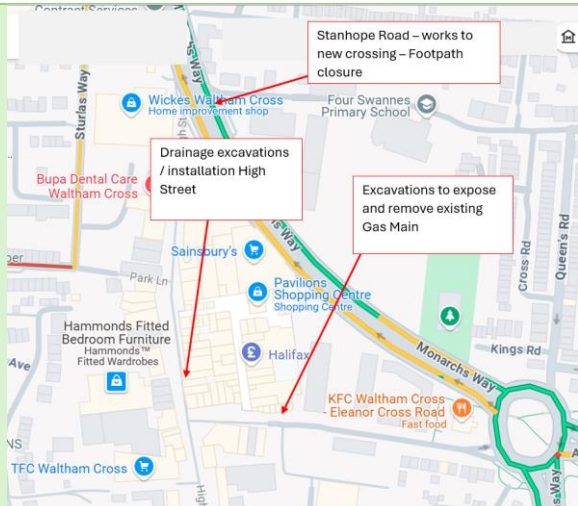	Eleanor Cross Road.	Continued work on new gas main installation	
	From Fishpools/High Street to Park Lane.	Installation of drainage manholes and subsequent extension of fencing along the High Street.	
Week ending 1 November	Monarchs Way	Excavation work to expose existing drainage network, ahead of connection with new drainage and manhole.	
	Stanhope Road	Continued installation of drainage, ducting and paving.	
	From Fishpools/High Street towards Eleanor Cross monument.	Continuation of gas main diversionary works.	
	From Eleanor Cross monument towards Fishpools	Completion of drainage installation. Drainage installation work towards Park Lane is ongoing.	
Week ending 25 October	Stanhope Road	Kerb removal and start of drainage installation, ahead of installation of new pedestrian crossing.	 <p>The map shows the Waltham Cross area with several roads and landmarks. Red boxes highlight specific construction sites: 'Stanhope Road - works to new crossing - Footpath closure' near the top right, 'Drainage excavations / installation High Street' in the center, and 'Excavations to expose and remove existing Gas Main' near the bottom right. Other labeled locations include Wickes Waltham Cross Home improvement shop, Four Swannes Primary School, Sainsbury's, Pavilions Shopping Centre, KFC Waltham Cross - Eleanor Cross Road Fast food, and various residential streets like Monarchs Way, Kings Rd, and Queen's Rd.</p>

	From Eleanor Cross Monument to Eleanor Cross Road	Excavation work for existing gas main diversion.	
	From Eleanor Cross monument to Park Lane	<p>Drainage installation started.</p> <p>Investigative work to prevent damage to existing cables. This works will continue in tandem with drainage installation.</p>	
On 12 September	High street – near Skills Hub	Groundbreaking event was held to mark the start of the works.	
From 4 September	Northern end of the High Street, including Waltham Cross High Street Car Park.	Site preparation – cordoning off and removal of street furniture.	
