






## Waltham Cross Regeneration Work: Progress Updates

Weekly updates			
2025			
Date	Location	Description	Photo
<b><u>Week ending 5 September</u></b>	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	Site clearance.	
		Drainage works.	
		Rain garden preparation works opposite bus station exit.	
		Excavation and preparation for footpath bays around monument.	
		Kerb installation works at Eleanor Cross Road and tie into Monarch's Way.	
	<b>Eleanor Cross Monument to Park Lane</b>	Kerb installation works.	
		Prepped and poured footpath bays.	
		Paving works.	
		Setting lids on utility and drainage chambers.	

	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Prepping and pouring footpath concrete bays.</p> <p>Paving works.</p> <p>Rain garden buildup finishing works.</p> <p>Kerb installation works.</p>	
	<p><b>Park Lane</b></p>	<p>Site clearance.</p> <p>Prepping for UKPN diversion/protection works.</p>	
	<p><b>Monarchs Way</b></p>	<p>Excavation and preparation for surfacing in centre reservation.</p> <p>Kerb installation at bottom end of centre reservation at KFC roundabout.</p> <p>Kerb installation at Eleanor Cross Road splitter going onto roundabout.</p> <p>Planter excavation works at splitter.</p> <p>Drainage works.</p>	

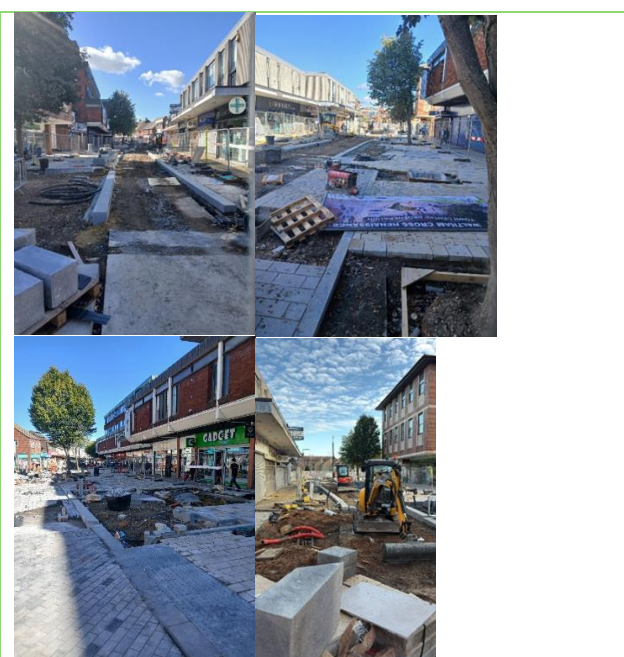

**Week  
ending 29  
August**

**Eleanor Cross  
Monument to  
Eleanor Cross  
Road**

Site clearance.

Drainage works.

Rain garden  
preparation works  
opposite bus station  
exit.



Excavation and  
preparation for  
footpath bays around  
monument.



Kerb installation  
works at KFC tie into  
Monarchs Way.



	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Prepping and pouring footpath concrete bays.</p> <p>Paving works.</p> <p>Finishing work for rain gardens.</p> <p>Kerb installation works.</p>	
	<p><b>Park Lane</b></p>	<p>Site clearance.</p> <p>Prepping and pouring footpath bays.</p>	
	<p><b>Eleanor Cross Monument to Eleanor Cross Road</b></p>	<p>Site clearance.</p> <p>Excavation preparation for surfacing work.</p> <p>White lining work on the carriageway.</p> <p>Kerb installation works.</p> <p>Planter excavation works.</p> <p>Drainage works.</p>	



<p><b><u>Week ending 22 August</u></b></p>	<p><b>Eleanor Cross Monument to Eleanor Cross Road</b></p>	<p>Continued construction of new splitter island at KFC.</p> <p>Replacement of damaged drainage kerbs.</p> <p>New road gully installation.</p> <p>New drainage network installation at KFC/approach to roundabout.</p> <p>New footpath construction and binder asphalt course.</p> <p>Ducting and foundation works.</p> <p>Excavation of tree bit on new splitter island.</p> <p>Kerb installation on new splitter island.</p> <p>Drainage kerb installation at KFC/approach to roundabout.</p> <p>Footpath concrete foundation at monument area.</p>	
	<p><b>Eleanor Cross Monument to Park Lane</b></p>	<p>Kerb installation works.</p> <p>Paving works.</p> <p>Installation of utility and drainage chamber covers.</p>	

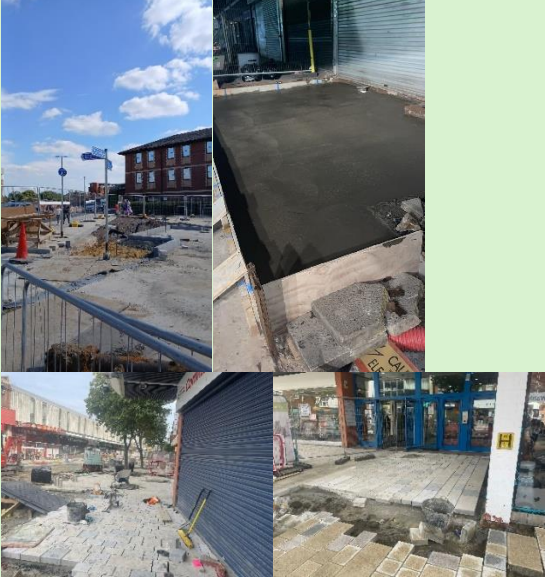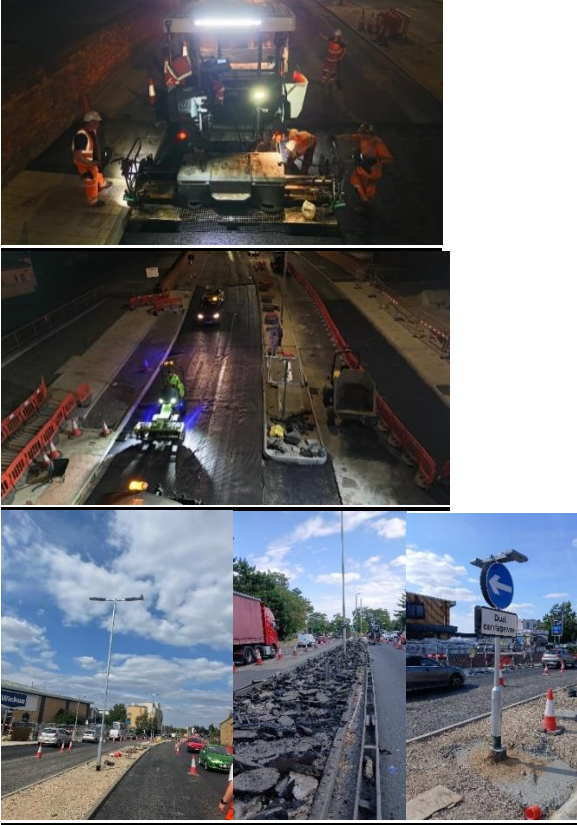	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Paving installation works.</p> <p>Kerb installation works.</p> <p>Concrete pouring for footpath foundations.</p> <p>Installation of streetlight ducting network.</p> <p>Installation of street light foundations.</p>	
	<p><b>Monarchs Way</b></p>	<p>Resurfacing works (Saturday and Sunday Night).</p> <p>Site clearance works.</p> <p>Installation of new streetlights.</p> <p>Installation of new road signage.</p>	



**Week  
ending 15  
August**

**Eleanor Cross  
Monument to  
Eleanor Cross  
Road**

Construction of new  
splitter island at KFC.

New footpath  
construction and  
installation of binder  
asphalt course.

Ducting and  
foundation works.

Footpath concrete  
foundation at  
monument area.





**Eleanor Cross  
Monument to  
Park Lane**

Kerb installation  
works.

Paving works.


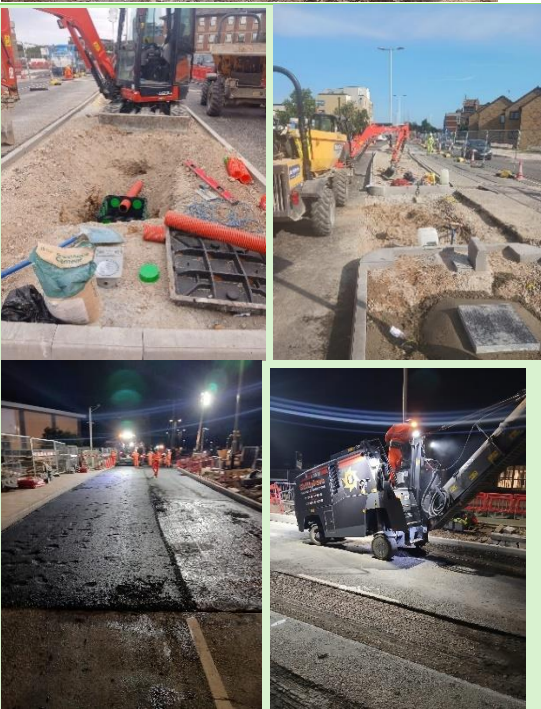

Installation of utility  
and drainage  
chamber covers.

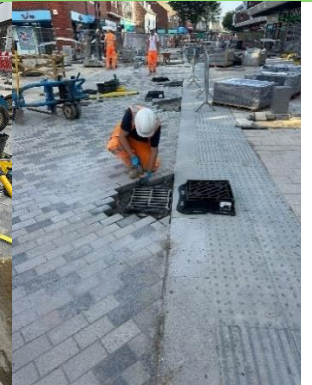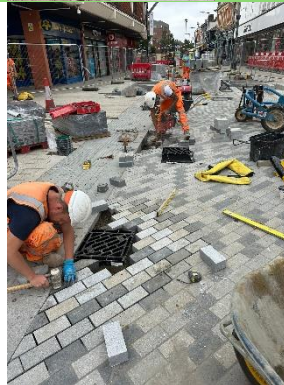


	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Paving installation works.</p> <p>Kerb installation works.</p> <p>Concrete pours to footpath foundations.</p> <p>Installation of streetlight ducting network.</p> <p>Installation of street light foundations.</p>	
	<p><b>Monarchs Way</b></p>	<p>Resurfacing works (Saturday and Sunday Night).</p> <p>Site clearance works to central reservation.</p> <p>Installation of new street light ducting.</p>	








	<b>Park Lane</b>	<p>Site clearance to footpath.</p> <p>Preparation of Concrete footpath foundations.</p> <p>Utility trial holes.</p>	
<b><u>Week ending 8 August</u></b>	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Kerb installation works.</p> <p>Relaying of York stone pavement.</p> <p>Street lighting and Monument lighting duct network installation.</p>	
	<b>Eleanor Cross Monument to Park Lane</b>	<p>Kerb installation works.</p> <p>Paving works.</p> <p>Concrete pouring for footpath foundations.</p>	



	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Paving installation works.</p> <p>Kerb installation works.</p> <p>Concrete pours to footpath foundations.</p> <p>Installation of Traffic signal Ducting network.</p> <p>Installation of street light ducting network.</p>	
	<p><b>Monarchs Way</b></p>	<p>Drainage works.</p> <p>Ducting network installation.</p> <p>Traffic signal socket and foundation installation.</p> <p>New Kerb alignment installation.</p> <p>Resurfacing works (Saturday and Sunday Night).</p>	
<p><b><u>Week ending 1 August</u></b></p>	<p><b>Eleanor Cross Monument to Eleanor Cross Road</b></p>	<p>Excavation and infill of rain garden and planter areas.</p> <p>Kerb and paving installation works.</p>	





		Street lighting and Monument lighting duct network installation.	
	<b>Eleanor Cross Monument to Park Lane</b>	<p>Kerb installation works.</p> <p>Paving works.</p> <p>Concrete Pours to footpath foundations.</p>	
	<b>Park Lane to northern end of the High Street (adjacent to Wickes)</b>	<p>Paving installation works.</p> <p>Kerb installation works.</p> <p>Concrete pours to footpath foundations.</p> <p>Installation of Traffic signal Ducting network.</p> <p>Installation of street light ducting network.</p>	

	<b>Monarchs Way</b>	<p>Site clearance.</p> <p>Drainage works.</p> <p>Ducting work across Monarch way.</p> <p>New Kerb alignment installation.</p> <p>Resurfacing works (Saturday and Sunday Night).</p>	 
<b><u>Week ending 25 July</u></b>	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Excavation and preparation for footpath bays.</p> <p>Kerb and paving installation works.</p> <p>Concrete pours to footpath foundation.</p> <p>Constuction of rain garden and planter areas.</p>	  

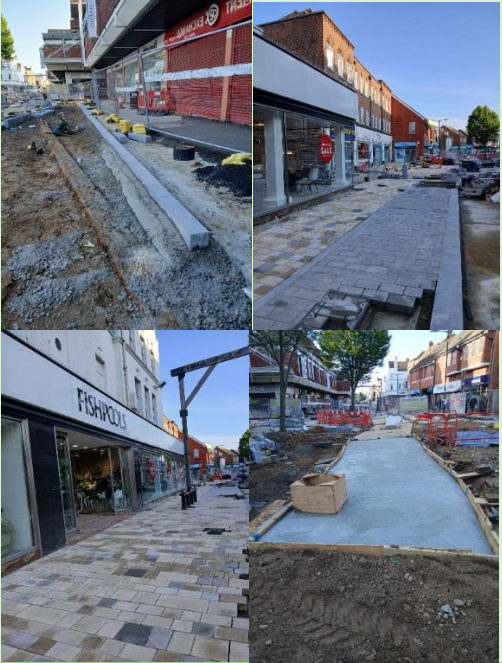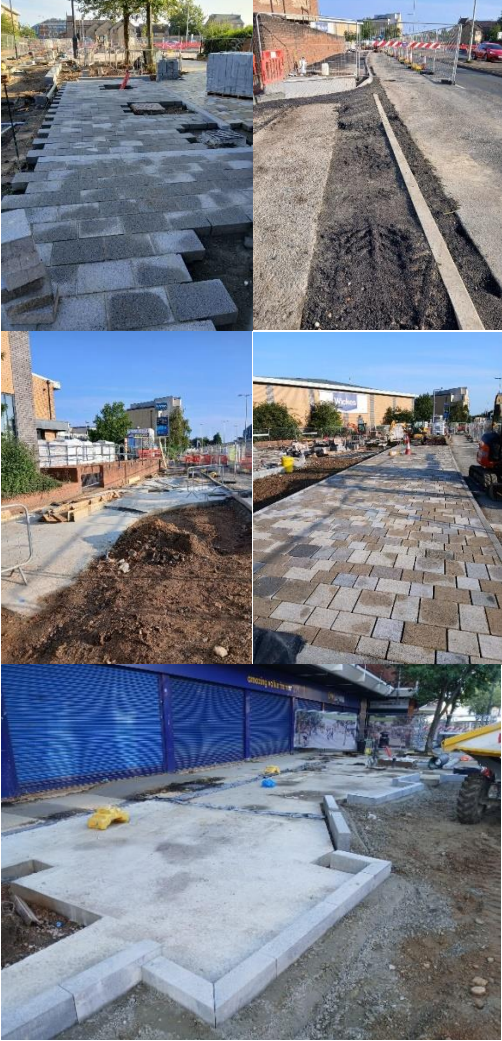


	<p><b>Eleanor Cross Monument to Park Lane</b></p>	<p>Kerb installation works.</p> <p>Paving works.</p> <p>Concrete Pours to road foundation.</p> <p>Concrete Pours to footpath foundations.</p>	
	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Paving installation works.</p> <p>Kerb installation works.</p> <p>Concrete pours to footpath foundations.</p> <p>Installation of traffic signal ducting network.</p> <p>Installation of traffic signal pole foundations.</p> <p>Installation of streetlight ducting network.</p> <p>Asphalt to footpath.</p> <p>Tactile installation.</p> <p>Drainage works.</p>	

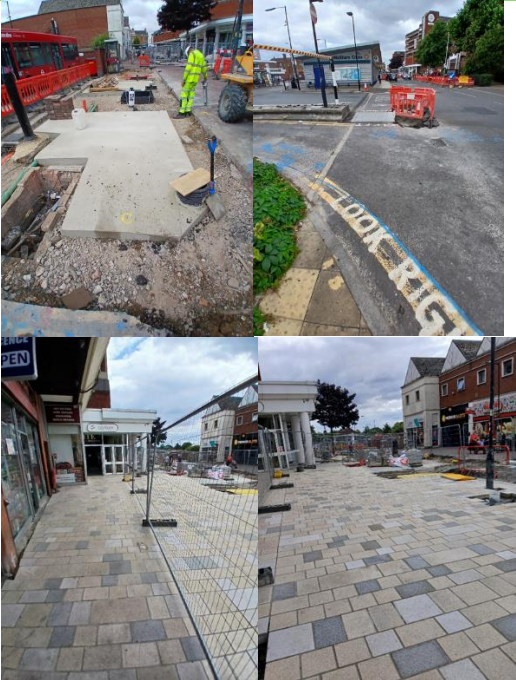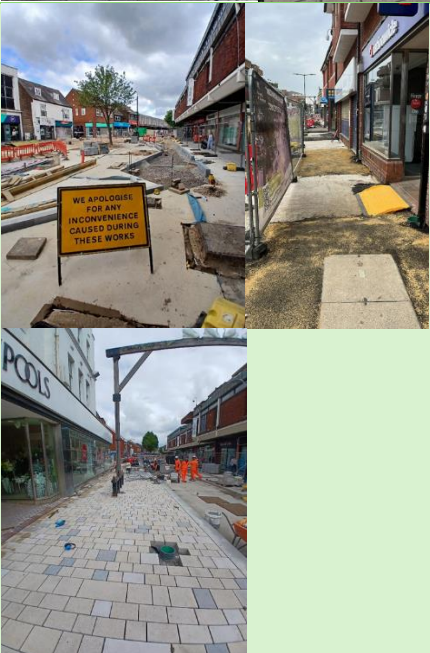	<b>Stanhope Road</b>	Removal of fencing.  Asphalt works to road.	
<b><u>Week ending 18 July</u></b>	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Tree cell works (Excavation, fill and build up).</p> <p>Excavation and preparation for footpath bays at bus station.</p> <p>Kerb and paving installation in front of shopping centre.</p>	
	<b>Eleanor Cross Monument to Park Lane</b>	<p>Kerb installation works.</p> <p>Low Impact Development (LID) setting and paving block installation.</p> <p>Addition of temporary ramp to the library after concrete paving foundation laid.</p>	



**Park Lane to  
northern end of  
the High Street  
(adjacent to  
Wickes)**

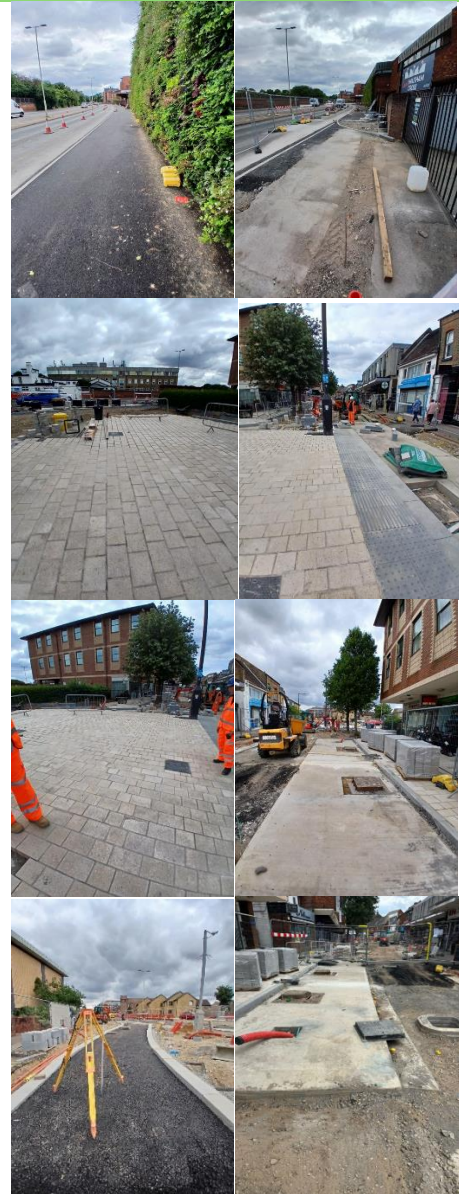

Paving installation.  
Asphalt laid to  
footpath on Monarchs  
Way.  
  
Surface bonding layer  
added to High Street  
and Monarchs Way.  
  
Kerb installation  
works.



**Stanhope Road**


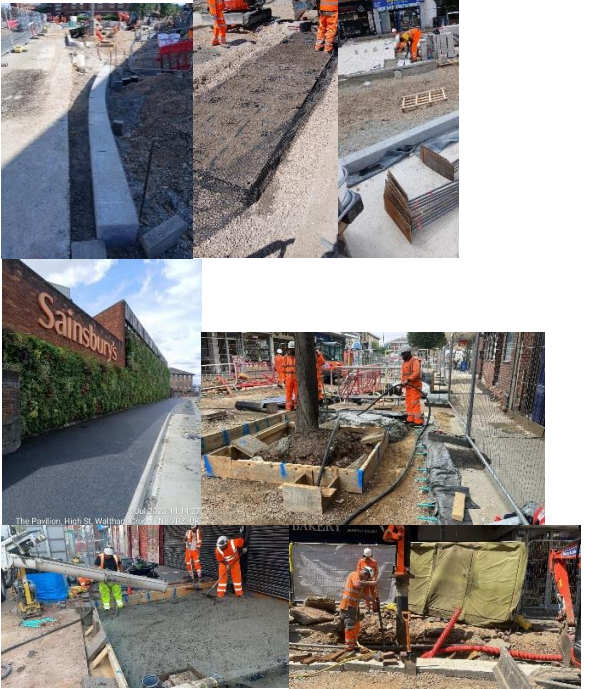
Top soil addition to  
verges.








<p><b><u>Week ending 11 July</u></b></p>	<p><b>Eleanor Cross Monument to Eleanor Cross Road</b></p>	<p>Site clearance.</p> <p>Drainage works.</p> <p>Tree cell build up finishing works.</p> <p>Excavation and preparation for footpath bays.</p> <p>Kerb and paving installation works.</p>	
	<p><b>Eleanor Cross Monument to Park Lane</b></p>	<p>Kerb installation.</p> <p>Streetlight ducting and sleeves installation.</p> <p>Paving works.</p>	






	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Paving installation.</p> <p>Preparation for binder on Monarch's Way Footpath.</p> <p>Preparation and pouring footpath concrete bays.</p> <p>Drainage works.</p>	
	<p><b>Stanhope Road</b></p>	<p>Planter finishing.</p> <p>Drainage works.</p>	
<p><b><u>Week ending 4 July</u></b></p>	<p><b>Eleanor Cross Monument to Eleanor Cross Road</b></p>	<p>Site clearance.</p> <p>Drainage works.</p> <p>Tree cell works (Excavation, fill and build up).</p> <p>Excavation and preparation for footpath bays at bus station.</p> <p>Kerb and paving installation in front of shopping centre.</p>	




	<p><b>Eleanor Cross Monument to Park Lane</b></p>	<p>Planter finishing works.</p> <p>Excavation and preparation for footpath bays.</p> <p>Kerb installation works.</p> <p>Lid setting and paving block installation.</p> <p>Trial hole works.</p>	
	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Excavation preparation for asphalt on footpath on Monarch's Way.</p> <p>Finishing road trim works to ahead of asphalt pouring on High Street.</p> <p>Paving installation works.</p> <p>Drainage works.</p> <p>Asphalt laid to footpath on Monarchs Way.</p> <p>Traffic signal box and duct installation.</p> <p>Kerb installation works.</p> <p>Tree cell works.</p> <p>Trial hole works.</p>	





	<b>Stanhope Road</b>	<p>Planter finishing works.</p> <p>Drainage works.</p>		
<b><u>Week ending 27 June</u></b>	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Site clearance works.</p> <p>Tree cell excavations works and installation.</p> <p>Work on street lighting and ducting installation.</p> <p>Drainage works.</p> <p>Paving and kerb installation</p>	  	
	<b>Eleanor Cross Monument to Park Lane</b>	<p>Site clearance and excavation to formation</p> <p>Planter excavation works and material fill.</p> <p>Excavation and preparation for footpath bays at shop fronts.</p> <p>BT Chamber adjustment and repair works.</p>		



	<b>Park Lane to northern end of the High Street (adjacent to Wickes)</b>	<p>Tree cell excavation and fill works (Material fill and build up).</p> <p>Excavation and prep for road formation and kerbs.</p> <p>Kerb and paving installation works.</p> <p>Excavation and preparation for footpath bays at shop fronts.</p> <p>Footpath clearance at Monarchs Way.</p> <p>Kerb installation on Monarchs Way.</p> <p>Installing traffic signal ducting and sleeves.</p> <p>Excavation ahead of footpath formation at Monarchs Way.</p>	
	<b>Stanhope Road</b>	<p>Planter excavation works (Material fill and build up).</p>	
<b><u>Week ending 20 June</u></b>	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Site clearance works.</p> <p>Kerb line preparation and installation.</p> <p>Excavation for tree cells.</p>	



		<p>Excavation and preparation for concrete bays and concrete pouring at bus shelter.</p> <p>Paving installed at footpath at bus shelter.</p>	
	<b>Eleanor Cross Monument to Park Lane</b>	<p>Excavation and preparation for footpath bays at shop fronts on east wing.</p> <p>Planter works.</p> <p>Excavating for planters and rain gardens.</p>	
	<b>Park Lane to northern end of the High Street (adjacent to Wickes)</b>	<p>Tree cell works.</p> <p>Excavation and preparation for road formation.</p> <p>Setting lids on chambers around site.</p> <p>Kerb and paving installation works.</p> <p>Excavation and preparation for footpath bays at shop fronts.</p> <p>Site clearance to footpath at Monarchs Way.</p>	

		<p>Kerb installation on Monarchs Way.</p> <p>Breaking out kerbs and existing asphalt at footpath on Monarchs Way.</p> <p>Installation of traffic signal ducting and sleeves.</p>	
	<b>Stanhope Road</b>	<p>Drainage works.</p> <p>Planter finishing works.</p> <p>Start of new planter excavation and preparation work.</p>	
<b><u>Week ending 13 June</u></b>	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Continued site clearance at bus station.</p> <p>Installing electric ducting and sleeves.</p> <p>Kerb and paving installation.</p> <p>Kerb installation at bus station.</p> <p>Footpath bay preparation and concrete pouring.</p> <p>Drainage works.</p>	

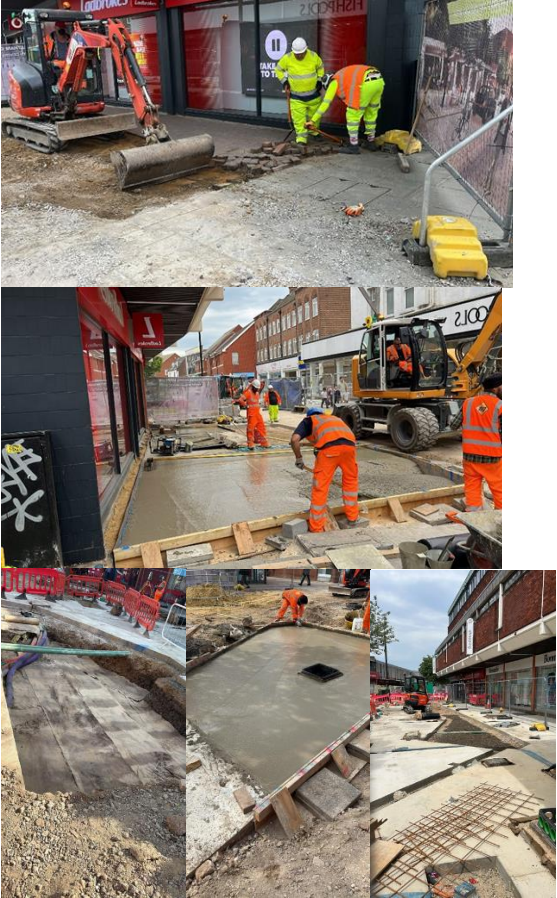

	<p><b>Eleanor Cross Monument to Park Lane</b></p>	<p>Concrete pouring for footpath and parking bays.</p> <p>Excavation for planters.</p> <p>Tree cell finishing works.</p>	
	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Excavation prep for footpath bays at Monarchs Way.</p> <p>Concrete pouring in footpath bays.</p> <p>Excavation for kerbs and road to be asphalted.</p> <p>Street lighting duct installation.</p> <p>Continued kerb and paving installation near underpass/Wickes.</p> <p>Planter works.</p> <p>Road planning works for new kerb line on Monarchs Way.</p>	

			
	<b>Stanhope Road</b>	<p>Demolition works for planter installation</p> <p>Material fill into planter area.</p> <p>Painting of underpass wall.</p>	



**Week  
ending 6  
June**


**Eleanor Cross  
Monument to  
Eleanor Cross  
Road**

Site clearance by Bus  
Station.

Installation of electric  
ducting and sleeves.

Drainage works.

Kerb and tactile  
paving installation.

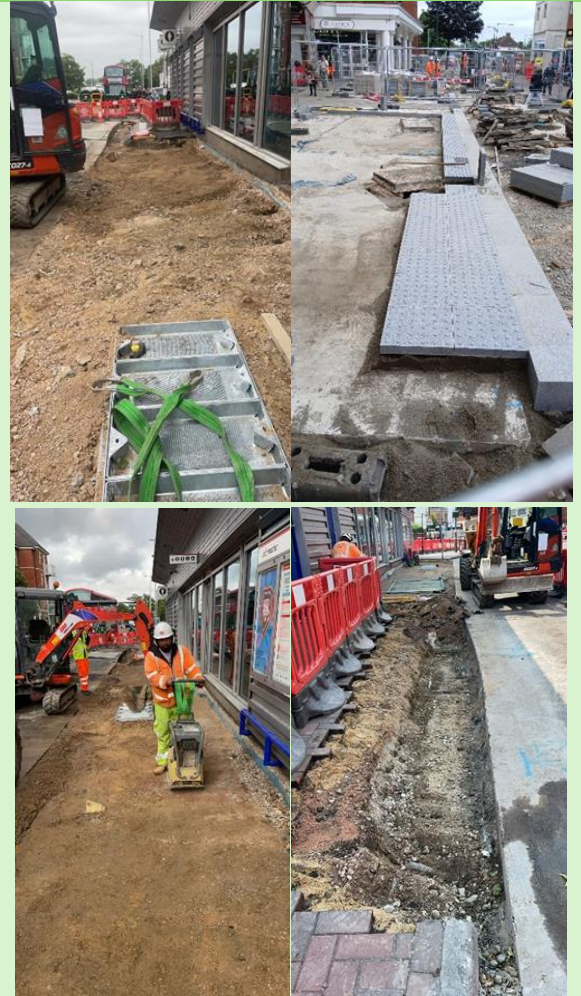


**Eleanor Cross  
Monument to  
Park Lane**

Excavation and  
preparation for  
installation of footpath  
and parking bays.

Concrete pouring on  
footpath and parking  
bays.

Finishing works for  
chamber lids.

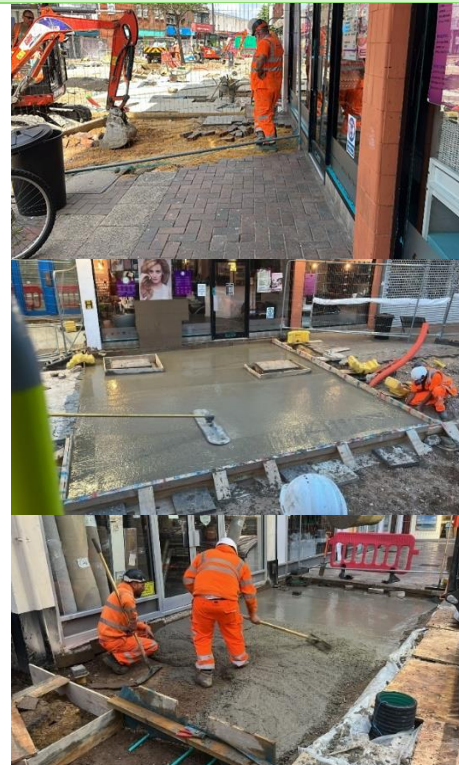

**Park Lane to  
northern end of  
the High Street  
(adjacent to  
Wickes)**

Excavation for  
footpath bays.

Pouring concrete in  
footpath bays.

Demolition of  
underpass walls  
completed.


Monarchs Way  
footpath site  
clearance.

Street lighting ducting  
installation.

Installation of paving  
near mobility shop.



Planter works.

Preparation to  
excavate road for  
asphalt installation.

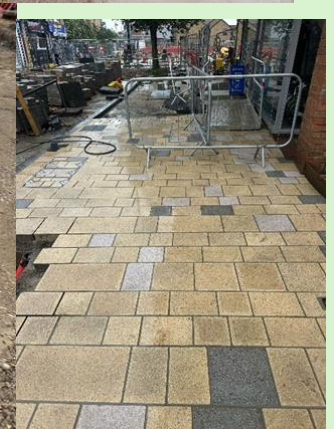




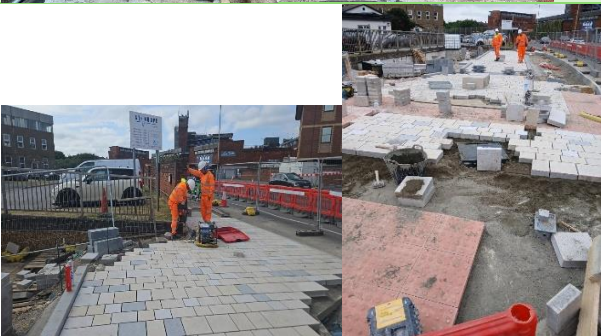
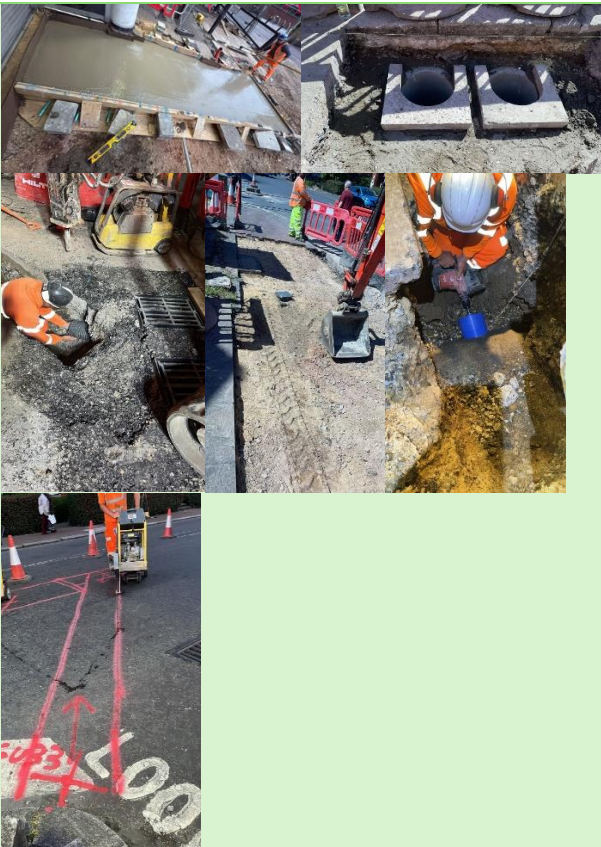


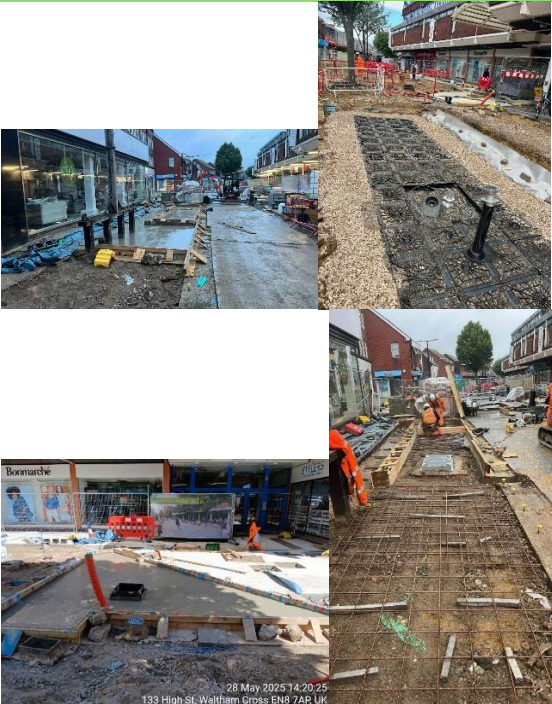	<b>Stanhope Road</b>	<p>Finishing works for chamber lids.</p> <p>Excavation for planters.</p> <p>Laying binder to footpath.</p> <p>Kerb installations.</p>	
<b><u>Week ending 30 May</u></b>	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Started site clearance at bus station.</p> <p>Continued excavation and preparation for footpath bays.</p> <p>Concrete pouring in footpath bays.</p> <p>Virgin Media chamber adjustment works.</p> <p>Drainage works.</p> <p>Street lighting cable installation.</p>	




	<p><b>Eleanor Cross Monument to Park Lane</b></p>	<p>Excavation digs and preparation for footpath bays at Fishpools and shopping centre.</p> <p>Concrete pouring in footpath and parking bays.</p> <p>Completion of tree cell works.</p> <p>Paving and kerb works continued between Fishpools and costa.</p>	
	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Tree cell works.</p> <p>Excavation preparation for footpath bays.</p> <p>Concrete pouring in footpath bays.</p> <p>Trial holes for subway wall demolition works.</p> <p>Subway wall demolition works.</p> <p>Monarchs Way footpath site clearance.</p> <p>Cable installation for street lighting installation.</p>	










	<b>Stanhope Road</b>	Continuation of paving works.	
<b><u>Week ending 23 May</u></b>	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Installation of streetlight cables.</p> <p>Grading and preparation for binder course.</p> <p>Continued work on footways.</p> <p>Break out and excavation drainage works for gullies</p> <p>installation and connection to mains in the road.</p> <p>UKPN preparation works.</p>	
	<b>Eleanor Cross Monument to Park Lane</b>	<p>Laying paving in road section between Fishpools and Costa Coffee.</p> <p>Concrete pouring on footway bays.</p> <p>Installation of subsoil to tree cells.</p>	

	<b>Park Lane to northern end of the High Street (adjacent to Wickes)</b>	<p>Concrete pouring on road and footway bays.</p> <p>Temporary surfacing in front of the Mobility Shop.</p>	
	<b>Stanhope Road</b>	<p>Preparation for footpath bay installation</p> <p>Concrete pouring on footpath bay.</p> <p>Start of kerb edging installation and paving works on the southside.</p>	
<b><u>Week ending 16 May</u></b>	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Excavation and preparation for footpath bays around the shopping centre.</p> <p>Pouring concrete in footpath bays.</p> <p>Break out and excavation of ground for drainage and gullies installation, and connection to the main run in the road.</p> <p>UKPN (UK Power Network) preparation works.</p>	



	<p><b>Eleanor Cross Monument to Park Lane</b></p>	<p>Paving work between Fishpools and Costa Coffee.</p> <p>Excavation and preparation for footpath bays in front of Bon Marche, CEX and shopping centre doors.</p> <p>Concrete pouring in footpath bays in front of Bon Marche, CEX and shopping centre doors.</p> <p>Site clearance by Fishpools.</p>	
	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Drainage works (gullies installation and connections).</p> <p>Excavation and preparation for road and footpath bays.</p> <p>Pouring concrete at road and footpath bays in front of La Valle.</p> <p>Continued underpass demolition works.</p>	
	<p><b>Stanhope Road</b></p>	<p>Preparation for footpath bay installation.</p> <p>Concrete pouring at footpath bay.</p> <p>Kerb and edging installation and paving works.</p>	

				
<b><u>Week ending 9 May</u></b>	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Preparation for footpath bays at pharmacy and shopping centre.</p> <p>Removal of bollards at fire brigade gate for footpath bay preparation.</p> <p>Excavation for streetlight cables along footpath on southside.</p> <p>Preparation of footpath for asphalt binder laying.</p> <p>Drainage excavations for gullies to be installed on the road.</p>	     	




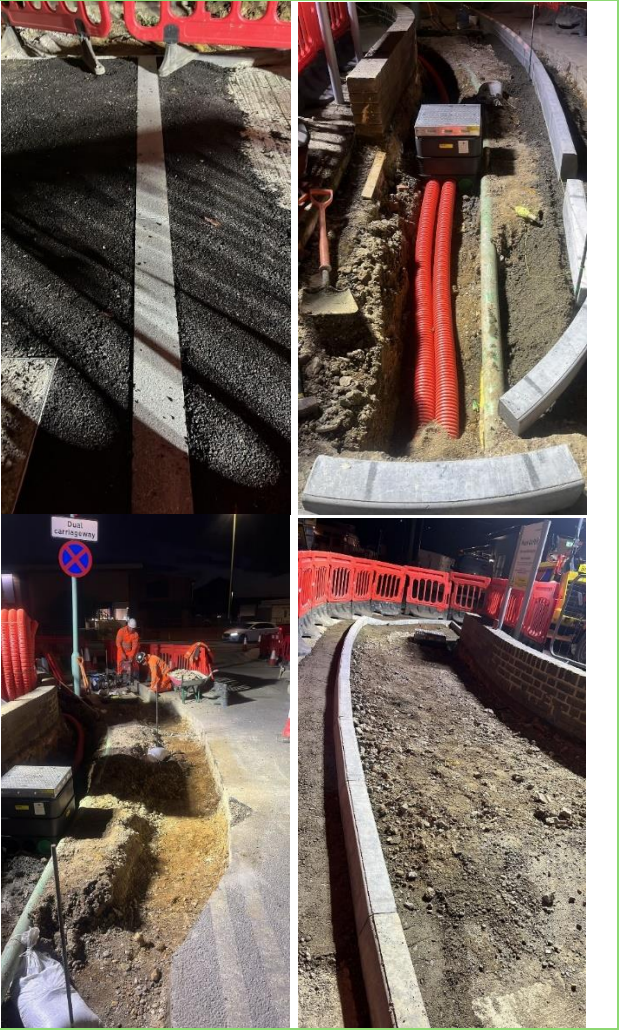
**Eleanor Cross  
Monument to  
Park Lane**

Installation of edgings, laying of paving and grouting in east wing market area and in front of Costa Coffee.

Excavation and preparation for footpath bays in front of Bon Marche.

Pouring of concrete in footpath bays in front of Bon Marche.



	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Drainage works (installation of gullies).</p> <p>Excavation and preparation for footpath bays in front of La Valle, in addition to concrete pouring on the footpath.</p> <p>Continued underpass demolition works.</p>	
	<p><b>Stanhope road</b></p>	<p>Excavation for traffic signal boxes, ducting, signpost sleeves and kerb installation near NHS entrance.</p> <p>Temporary tarmac laid on Northside near substation to open access for pedestrians.</p>	



**Week  
ending 2  
May**

**Stanhope Road**

**South of Junction**

Pedestrian walkways altered.

Excavation and Subbase laid for Footpath construction.

Footpath concrete paving foundations poured.

**North of Junction**

Clearance of existing footpath and kerb line.

Excavation and Subbase laid for Footpath construction.

New kerb line installed.

Concrete paving foundations poured.



**Park Lane to  
northern end of  
the High Street  
(adjacent to  
Wickes)**

Excavation for kerb braces, parking bays and footpath concrete foundations.






Concrete pours for footpath bays and kerb braces.

Drainage works.




Demolition works to existing subway wall.


New street light network cables installed.






		Continued work on high voltage cable diversion and reinstatement.		
	<b>Eleanor Cross Monument to Park Lane</b>	<p>Footpath paving concrete foundations poured in front of Savers doorway and shop front.</p> <p>Block Paving installed to Market area.</p> <p>New street lighting network cable installed.</p> <p>Removal of existing Street lights.</p>	  	
	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Concrete paving foundations poured in front of shop fronts and doorways at Pavilions Mobile Tech and Handerson's news agents.</p> <p>Excavation and concrete paving foundation works progressed in front of Pavilions shopping centre and in front on Timpson.</p> <p>Removal of existing streetlights.</p>	 	






	<b>Eleanor Cross Road</b>	<p>Traffic management layout change.</p> <p>Footpath temporarily reopened.</p> <p>Existing footpath excavated and subbase laid.</p> <p>Clearance of existing block paving.</p> <p>Utility covers set to correct levels.</p>	
<b><u>Week ending 25 April</u></b>	<b>Stanhope Road</b>	<p>Demolition of Existing underpass walls.</p> <p>Subbase laid for Footpath construction.</p> <p>Removal of existing streetlighting.</p> <p>Installation of new street lighting cables.</p> <p>Installation of traffic signal control sockets and foundations.</p> <p>Removal of existing kerb line.</p>	
	<b>Park Lane to northern end of the High Street (adjacent to Wickes)</b>	<p>Excavation for kerb braces, parking bays and footpath concrete foundations.</p> <p>Concrete pours for footpath bays and kerb braces.</p> <p>Drainage works.</p> <p>Demolition works to existing subway wall.</p>	




		<p>New street light network ducts installed.</p> <p>Continued excavation for high voltage cable diversion.</p> <p>High voltage cable diversion.</p> <p>Lowering of utility chambers.</p>	
	<b>Eleanor Cross Monument to Park Lane</b>	<p>Work progressed further along shop frontages.</p> <p>Continued excavation to Footpath in front of Costa coffee.</p> <p>Concrete foundations poured.</p> <p>Excavation to Footpath in front of Savers Phase 1 and concrete foundations poured.</p> <p>New Street lighting network ducts installed.</p> <p>Removal of existing streetlights.</p>	
	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Works in front of shop frontages progressed to new sections.</p> <p>Continued work on excavation of footpath and parking bays, subbase laid, and concrete foundations pouring.</p> <p>Removal of existing Street lights.</p>	








	<b>Eleanor Cross Road</b>	<p>Existing footpath excavated and subbase laid.</p> <p>Tactile crossing installation.</p> <p>Asphalt base course laid.</p> <p>Streetlight network ducting installed.</p> <p>Removal of old street furniture.</p>	
<b><u>Week ending 18 April</u></b>	<b>Stanhope Road</b>	<p>Concrete footpath foundations prepped and poured.</p> <p>Traffic signal ducting installed.</p> <p>Demolition of existing subway parapet wall.</p> <p>Site clearance of existing kerb line.</p> <p>Trial holes along existing footpath.</p>	
	<b>Park Lane to northern end of the High Street (adjacent to Wickes)</b>	<p>Excavation for kerb braces, parking bays and footpath concrete foundations.</p> <p>Concrete pours for footpath bays and kerb braces.</p> <p>Drainage works.</p> <p>Demolition works to existing subway wall</p> <p>New street light network ducts installed.</p> <p>Trial Holes in preparation of high</p>	





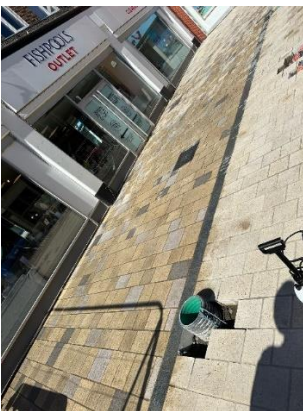


		voltage cable diversion.	
	<b>Eleanor Cross Monument to Park Lane</b>	<p>Work area progressed to shop frontages.</p> <p>Excavation of footpath in front of Costa Coffee.</p> <p>Concrete foundations poured.</p> <p>New street lighting network ducts installed.</p>	
	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Works progressed to shop frontages.</p> <p>Excavation of footpath and parking bays to formation and subbase laid.</p>	
	<b>Eleanor Cross Road</b>	<p>New 80 metre Kerb line installed.</p> <p>New street light network ducting installed.</p> <p>New road drainage gullies installed and connected to live main.</p> <p>Footpath widening excavated and subbase laid.</p>	





		Existing footpath excavated and subbase laid.	
<b><u>Week ending 11 April</u></b>	<b>Stanhope Rd</b>	<p>Concrete pouring footpath foundations.</p> <p>Cable installation for new traffic lights.</p> <p>Site clearance of infilled underpass.</p>	 
	<b>Park Lane to northern end of the High Street (adjacent to Wickes)</b>	<p>Excavation for parking bays, kerb braces and footpath concrete foundations (concrete pouring was also carried out for the last two activities).</p> <p>Continued drainage works and excavation for tree planting areas.</p>	


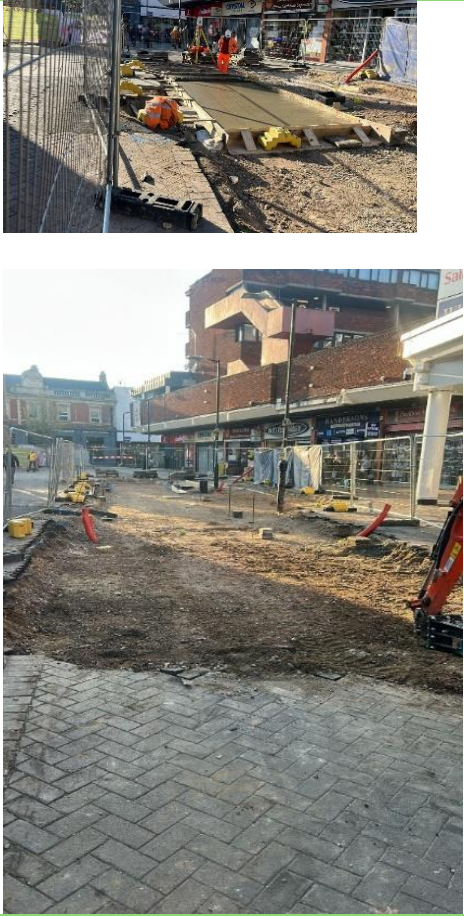
			  
	<b>Eleanor Cross Monument to Park Lane</b>	<p>Investigative work in front of Fishpools with trial holes.</p> <p>Trials holes were also drilled to check for drainage.</p> <p>New paved area in front of Fishpools was reopened.</p>	 
	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Pouring of concrete slab for new parking and road bays.</p> <p>Continued excavation and development of the new road, and alignment work for the new kerb.</p>	 



	<b>Eleanor Cross Road</b>	<p>Work in this section is being approached in two phases.</p> <p>For the first phase, several activities were undertaken this week including relocation of temporary traffic lights, start of drainage works, clearance of existing kerb lines and installation of new kerb lines.</p>	 
<b><u>Week ending 4 April</u></b>	<b>Stanhope Road</b>	Excavation of existing footpath and installation of new concrete footpath foundation.	 
	<b>Park Lane to northern end of the High Street (adjacent to Wickes)</b>	<p>Excavation for kerb braces, parking bays and footpath concrete foundations.</p> <p>Concrete pouring for footpath bays and kerb braces.</p> <p>Street lighting removal and installation of temporary solar powered street lighting.</p> <p>Continuation of drainage works.</p>	  

	<b>Eleanor Cross Monument to Park Lane</b>	<p>Removal of street lighting and installation of temporary solar powers lighting.</p> <p>Trial hole drilling to check for existing drainage.</p> <p>Application of protective sealant to paving.</p>	
	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Concrete slab pouring for parking and road bays, and continued excavation and development of the new road.</p>	




	<b>Eleanor Cross Road</b>	<p>Installation of traffic management. Removal of street lighting, furniture and splitter island.</p> <p>Following removal of the splitter island, Asphalt was reinstated.</p>	
<b><u>Week ending 28 March</u></b>	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Road formation work, installation of streetlight cables and sleeves and concrete slab pouring on footpath bays.</p>	

**Eleanor Cross Monument to Park Lane**

Finalised grouting and completed paving and kerbing in front of Fishpools.

Excavation and installation of tree cells in front of the shopping centre.

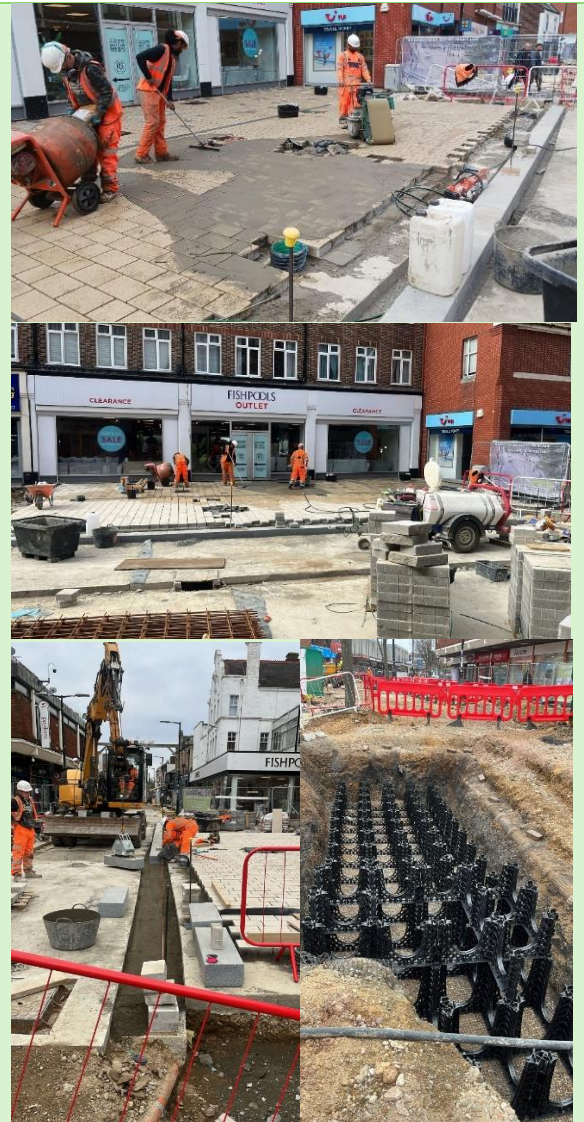


**Park Lane to northern end of the High Street (adjacent to Wickes)**



Excavation for tree cell installation, backfilling of diverted electricity cable, excavation for kerb braces, parking bays and footpath concrete foundations.

Concrete was poured on installed footpath bays and braces.

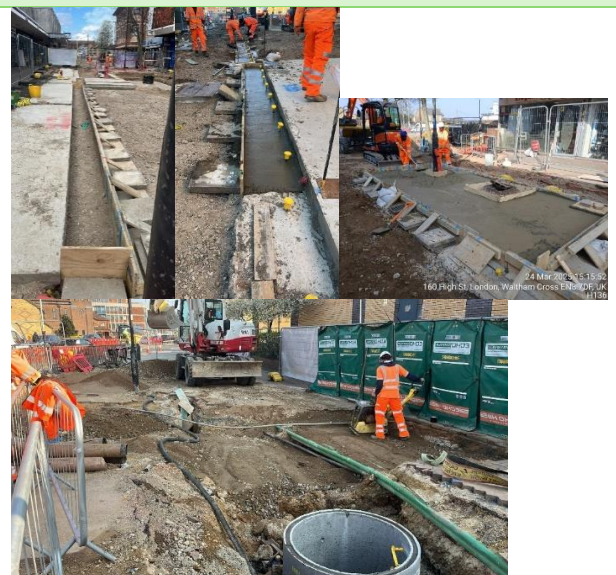Drainage works continued and a temporary footpath was set up outside One Beyond.










			
	<b>Stanhope Road</b>	Excavation and installation of new traffic light cables and kerbs	

			
<b><u>Week ending 21 March</u></b>	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	<p>Removal of existing paving, and excavation for new road and kerb.</p> <p>Excavation work for new parking bays.</p>	
	<b>Eleanor Cross Monument to Park Lane</b>	<p>Paving installation in front of Fishpools.</p> <p>Existing electricity utility diversion work.</p> <p>Excavation for new tree pits and rain garden drainage.</p>	



			
	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Continued drainage works and excavation for kerb braces, new road alignment, parking bays and footpath concrete foundations.</p> <p>Excavation for new tree pits and rain garden drainage.</p> <p>Diversion of existing electricity utility. Installation of new street lighting power cables.</p>	

	<b>Stanhope Road</b>	<p>Nighttime work for drainage installation and new traffic signal cabling installation.</p> 
<b><u>Week ending 14 March</u></b>	<b>Park Lane to northern end of the High Street (adjacent to Wickes)</b>	<p>Continuation of drainage works, excavation for kerbs, parking bays and rain gardens.</p> <p>Installation of concrete protection around utilities.</p> 
		<p>Concrete pouring for footpath foundation, and continued work on placement and compaction of road stone.</p> <p>Continued excavation for rain garden.</p> 




## Stanhope Road

New paving cleaned and protective sealant installed.

Work fencing was removed and the new pedestrian paving on the northern side of the junction was opened.

Preparation on the opposite side of the road for drainage and kerb works next week.

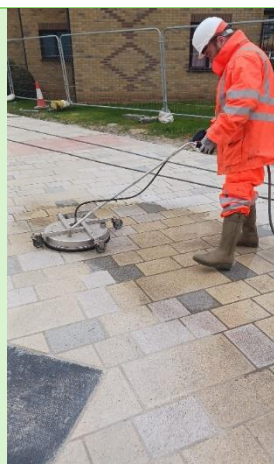




## Eleanor Cross Monument to Park Lane

Concrete pour on footpath bays, drainage works and installation of new cables.





Preparation works in front of Fishpools to begin work on kerbs, edgings and block paving next week.



			
		Continued excavation for electricity cable diversion and excavation for new planter area.	  
	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	Drainage works (saddle connections to carrier drainage pipe). Site clearance in preparation for more drainage work next week.	  
<b><u>Week ending 7 March</u></b>	<b>Stanhope Road</b>	Continued installation of new paving.	 



			 
	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Workers have started to excavate for the new 'rain gardens'.</p>	 
		<p>Continuation of work on the underpass with stone infill completed, and continued demolition of existing walls.</p>	

		Existing utility cables lowered to enable road construction. Laying of road stone.	
	<b>Eleanor Cross Monument to Park Lane</b>	Additional pedestrian crossover points temporarily installed	
		Excavation to divert high voltage electricity cable	
		Cable ducting work to new street lighting installation.	



		Continued work on concrete pouring on road and footpath bays, and excavation for planter area has started.	
	<b>Eleanor Cross Monument to Eleanor Cross Road</b>	Continuation of drainage works and trial excavations to locate existing utility pipes	
<b><u>Week ending 28 February</u></b>	<b>Northern end of the High Street (new pedestrian crossings)</b>	Continuation of paving slab installation at the new crossing point in Stanhope Road	
	<b>Northern end of the High Street (underpass)</b>	Work has continued to backfill the now decommissioned underpass at Monarchs Way	


	<b>Park Lane to northern end of the High Street (adjacent to Wickes)</b>	Continuation of work to lower existing utility ducts to accommodate new road surface.	
	<b>Eleanor Cross Monument to Park Lane</b>	Concrete started to be poured along the High Street to serve as the new road foundation. Preparation work has continued to install new paving outside Fishpools.	 
<b><u>Week Ending 21 February</u></b>	<b>Stanhope Road</b>	Continued work on new paving installation, including the addition of tactile paving.	






	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Work on breaking down the ramps that used to serve the former underpass has continue alongside backfilling to bring the ramp up to street level.</p>	
	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Lowering of existing utility ducts to accommodate new road surface.</p>	
	<p><b>Eleanor Cross Monument to Park Lane</b></p>	<p>Old paving removed from outside Fishpools. Concrete bays have been installed outside the shop, these will support the new foundation and paving.</p>	




<p><b><u>Week Ending 14 February</u></b></p>	<p><b>Stanhope Road</b></p>	<p>New paving slabs installed at the new pedestrian crossing.</p>	
	<p><b>northern end of the High Street (adjacent to Wickes)</b></p>	<p>Infilling of former underpass ramp section with stones. This is being done to bring this section up street level.</p>	
	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Continued excavation work for new drainage runs. This is progressing well with 90% of the drainage now installed.</p>	








	<b>Eleanor Cross Monument to Park Lane</b>	Concrete base for the new road was poured and levelled. These new concrete bays will serve as the foundation for the new paving slabs.	
<b><u>Week Ending 7 February</u></b>	<b>Stanhope Road</b>	Concrete foundations for the new pedestrian crossing laid. Traffic light bases installed and tested.	
	<b>Park Lane to northern end of the High Street (adjacent to Wickes)</b>	Continued excavation for installation of drainage runs along this location.	
	<b>Eleanor Cross Monument to Park Lane</b>	Installation of shutter frames on the ground to support the paving's concrete foundations.	




<p><b><u>Week Ending 31 January</u></b></p>	<p><b>Stanhope Road</b></p>	<p>Started to install concrete foundations to connect the new paving (also being installed) to the new pedestrian crossing.</p>	
	<p><b>Stanhope Road</b></p>	<p>Continued work to break up ramp that serviced the underpass. At the same time, drainage is also being installed next to the former underpass.</p>	
	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Continued excavation and installation of new drainage.</p>	
	<p><b>Eleanor Cross Monument to Park Lane</b></p>	<p>Continued work on the installation of concrete foundations for the new road. Ground levelling work is ongoing along with installation of bases for new lighting columns.</p>	



<b><u>Week Ending 24 January</u></b>	<b>Stanhope Road</b>	Decommissioned underpass has been filled with concrete. Work in progress to break up the concrete ramps that serviced the underpass ahead of filling these sections.	
	<b>Stanhope Road</b>	Kerbs have been installed in preparation for concrete pouring for new street foundations.	
	<b>Stanhope Road</b>	Ground preparation work to install the new pedestrian crossings has commenced.	
	<b>Park Lane to northern end of the High Street (adjacent to Wickes)</b>	Drainage installation	
	<b>Eleanor Cross monument to Park Lane</b>	Drainage work in this section has been completed. Concrete started being poured for foundation of the new road	

<p><b><u>Week Ending 17 January</u></b></p>	<p><b>Stanhope Road</b></p>	<p>Work on filling underpass has commenced. This work took three days to complete.</p>	 
<p><b>Week ending 10 January</b></p>	<p><b>Stanhope Road</b></p>	<p>Wooden shutters installed in underpass to support concrete filling.</p>	
	<p><b>Park Lane to northern end of the High Street (adjacent to Wickes)</b></p>	<p>Start of planned drainage installation to go around existing utilities.</p>	
	<p><b>Eleanor Cross Road Monument to Park Lane</b></p>	<p>Excavation for new road foundation and streetlights as well as ducting to power new streetlights.</p>	


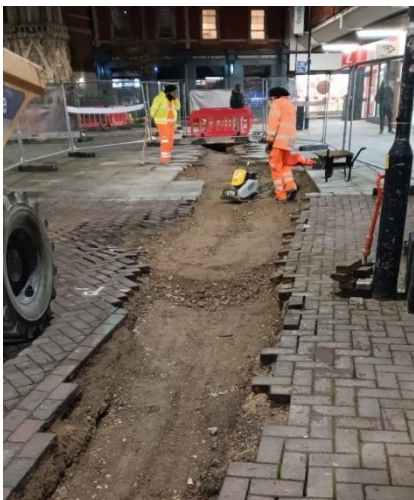


2024					
Week ending 13 December	Monarchs Way	All road closure barriers were removed to facilitate traffic flow during the Christmas period when work in the town centre will be suspended.			
	Stanhope Road	Pipes and ducting installed at Monarchs Way underpass. Work commenced to install shutters that will retain the concrete which is to be poured in a few weeks.			
	Park Lane to Monarchs Way	Investigative work for existing utility duct that needs to be lowered in this area.			
	Eleanor Cross Road Monument to northern end of the High Street (adjacent to Wickes)	Digging to accommodate foundations of the new road commenced.			





	<b>Eleanor Cross Road Monument to Park Lane</b>	<p>Work to lower existing utility duct ahead of new pavement installation.</p> <p>Continuation of drainage installation.</p>	 
<b>Week ending 6 December</b>	<b>Monarchs Way</b>	Road works on Monarchs Way completed.	
	<b>Stanhope Road</b>	Preparation ahead of disconnection of electrical services in the underpass linking Stanhope Road with the High Street.	
	<b>Park Lane to Monarchs Way</b>	Removal of existing paving and setting out of new lines for proposed drainage locations.	
	<b>Eleanor Cross Monument to Park Lane</b>	Continued work to lower existing utility ducts, and work to start reducing the existing ground to the correct level for the new road.	




				
<b>Week ending 29 November</b>	<b>Stanhope Road</b>	Installation of new kerbs and bases for the new traffic lights.		
	<b>Park Lane to Monarchs Way</b>	Extension of fencing lines ahead of removal of existing pavement.		
	<b>Monarchs Way</b>	Drainage installation completed.		
	<b>Northern end of the High Street</b>	Section of drainage installation completed.		




	<b>Near Queen Eleanor Monument Towards northern end of the High Street</b>	Lowering of existing utility duct, and continued installation of drainage.	
	<b>From Eleanor Cross Monument to Park Lane</b>	Completion of gas main installation and backfilling, and removal of fencing from related section.	
<b>Week ending 22 November</b>	<b>Stanhope Road</b>	Excavations on the South Bound Carriageway to install the new kerb line and, excavations to allow the new traffic lights to be powered. In tandem, excavations have also commenced on the opposite side, (next to Wicks) for drainage and new kerbs.	
	<b>Fishpools/High Street to Eleanor Cross Road</b>	Preparation ahead of final connection of gas main, with testing and backfilling continuing in tandem.	



	<b>Northern end of the High Street</b>	Drainage installation planning to avoid existing utilities		
	<b>From Eleanor Cross Monument to Park Lane</b>	Continuation of drainage installation		
<b>Week ending 15 November</b>	<b>Stanhope Road</b>	Works on the new pedestrian crossing		
	<b>From Fishpools/High Street to Eleanor Cross Road</b>	Backfilling and testing of installed gas main		

	<b>Northern end of High Street from Waltham Cross Bakery to Wicks</b>	Vacuum excavation ahead of drainage installation.		
	<b>From Eleanor Cross Monument to Park Lane</b>	Excavation to reveal existing ducts and pipes, ahead of installation of new ones.		
<b>Week ending 8 November</b>	<b>Monarchs Way</b>	New Manhole was installed within the north bound carriage way		
	<b>Stanhope Road</b>	Installation of manholes. In addition, installation of ducts and pipes to feed new traffic light electricity continues.		
	<b>Eleanor Cross Road.</b>	Continued work on new gas main installation		
	<b>From Fishpools/High Street to Park Lane.</b>	Installation of drainage manholes and subsequent extension of fencing along the High Street.		
<b>Week ending 1 November</b>	<b>Monarchs Way</b>	Excavation work to expose existing drainage network, ahead of connection with new drainage and manhole.		

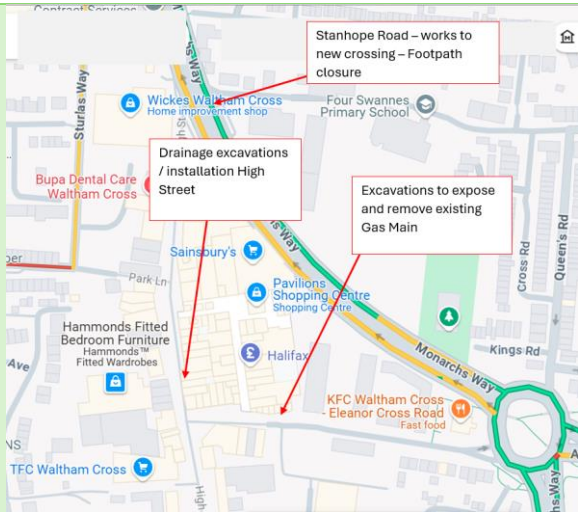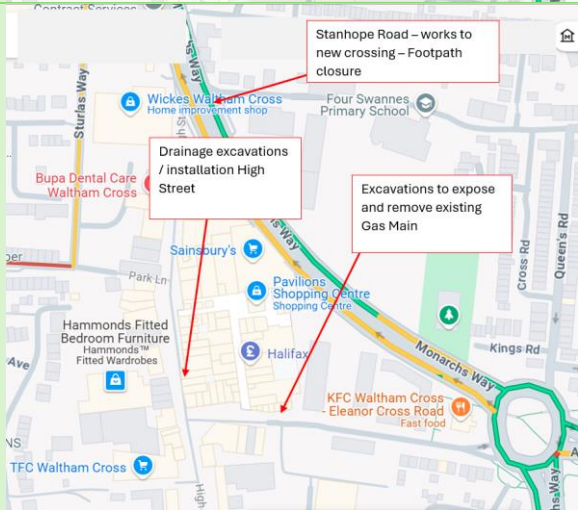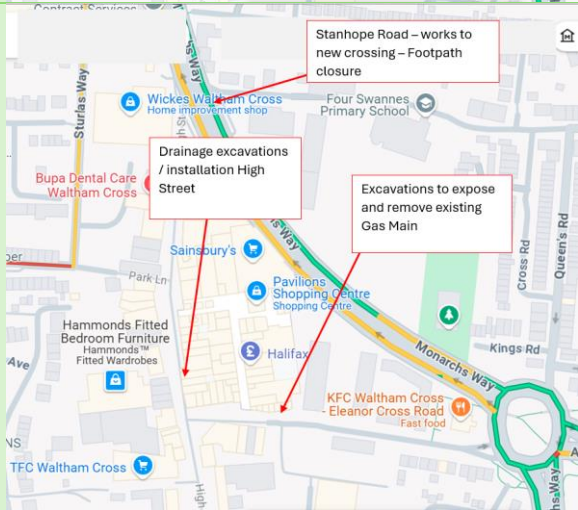

	Stanhope Road	Continued installation of drainage, ducting and paving.	
	From Fishpools/High Street towards Eleanor Cross monument.	Continuation of gas main diversionary works.	
	From Eleanor Cross monument towards Fishpools	Completion of drainage installation. Drainage installation work towards Park Lane is ongoing.	
<b>Week ending 25 October</b>	Stanhope Road	Kerb removal and start of drainage installation, ahead of installation of new pedestrian crossing.	
	From Eleanor Cross Monument to Eleanor Cross Road	Excavation work for existing gas main diversion.	
	From Eleanor Cross monument to Park Lane	<p>Drainage installation started.</p> <p>Investigative work to prevent damage to existing cables. This works will continue in tandem with drainage installation.</p>	

<p><b>On 12 September</b></p>	<p>High street – near Skills Hub</p>	<p>Groundbreaking event was held to mark the start of the works.</p>	
<p><b>From 4 September</b></p>	<p>Northern end of the High Street, including Waltham Cross High Street Car Park.</p>	<p>Site preparation – cordoning off and removal of street furniture.</p>	
